

Holloway Park, London

Construction Monitoring Report

Client: London Square
Ref: CM138-22405-R0
Date: 6 August 2026
Note by: Sebastian Sloan, BSc TechIOA, Acoustics Consultant
Reviewed by: Anthony Coraci, MSc DipIOA, Senior Acoustics Consultant

1. INTRODUCTION

- 1.1 This Technical Note sets out results of the construction monitoring being carried out at the above site between Monday 13th & Saturday 25th July 2026. The monitoring is being carried out in general agreement with the methodology in the current Section 61 Consent between the London Borough of Islington and London Square.

2. SITE ACTIVITIES

- 2.1 The following activities have been carried during the period covered by this report, in addition to the usual use of the Haul Road with site vehicles, and mobile plant used around the site:


- Fixing works and brickwork at Blocks C, D, E1 & E2.
- Block E window installations.
- Marketing suite construction within the proximity of Block C1 (handed over 21st July)
- Brickwork and internal fitout across Blocks C1, D1, D2, D3, all E blocks

3. MONITORING DATA

3.1 This section sets out a summary of the monitoring data that has been recorded onsite and provides a discussion of any exceedances and best practicable means incorporated by the site team if exceedances were believed to be construction related.


Dust Monitoring Results

Location 1 (meter ref. TNO3599)

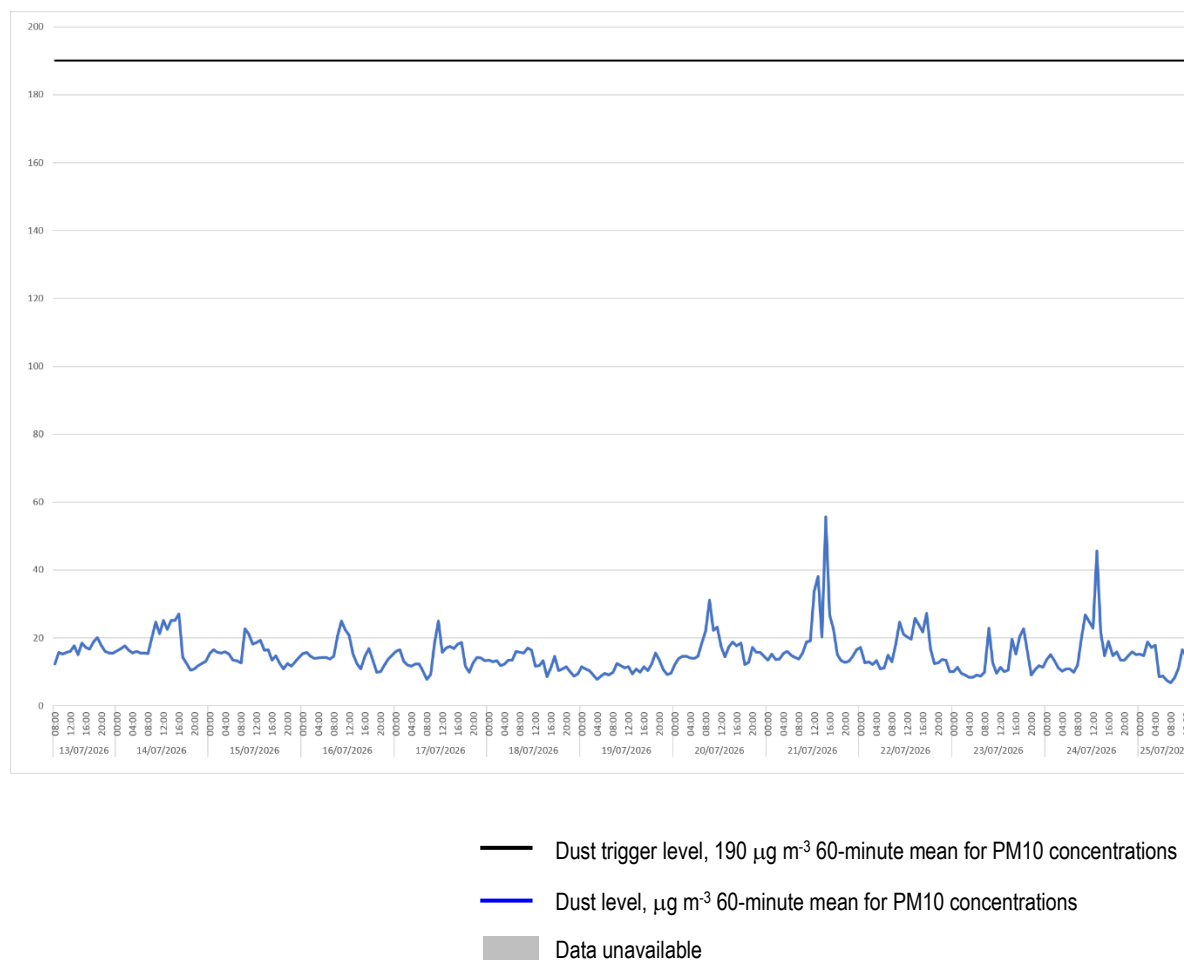


3.2 There was 100% data coverage during the monitoring period. There were no exceedances of the dust trigger level of 190 $\mu\text{g m}^{-3}$ recorded at this location during construction hours.

Location 2 (meter ref. TNO4719)

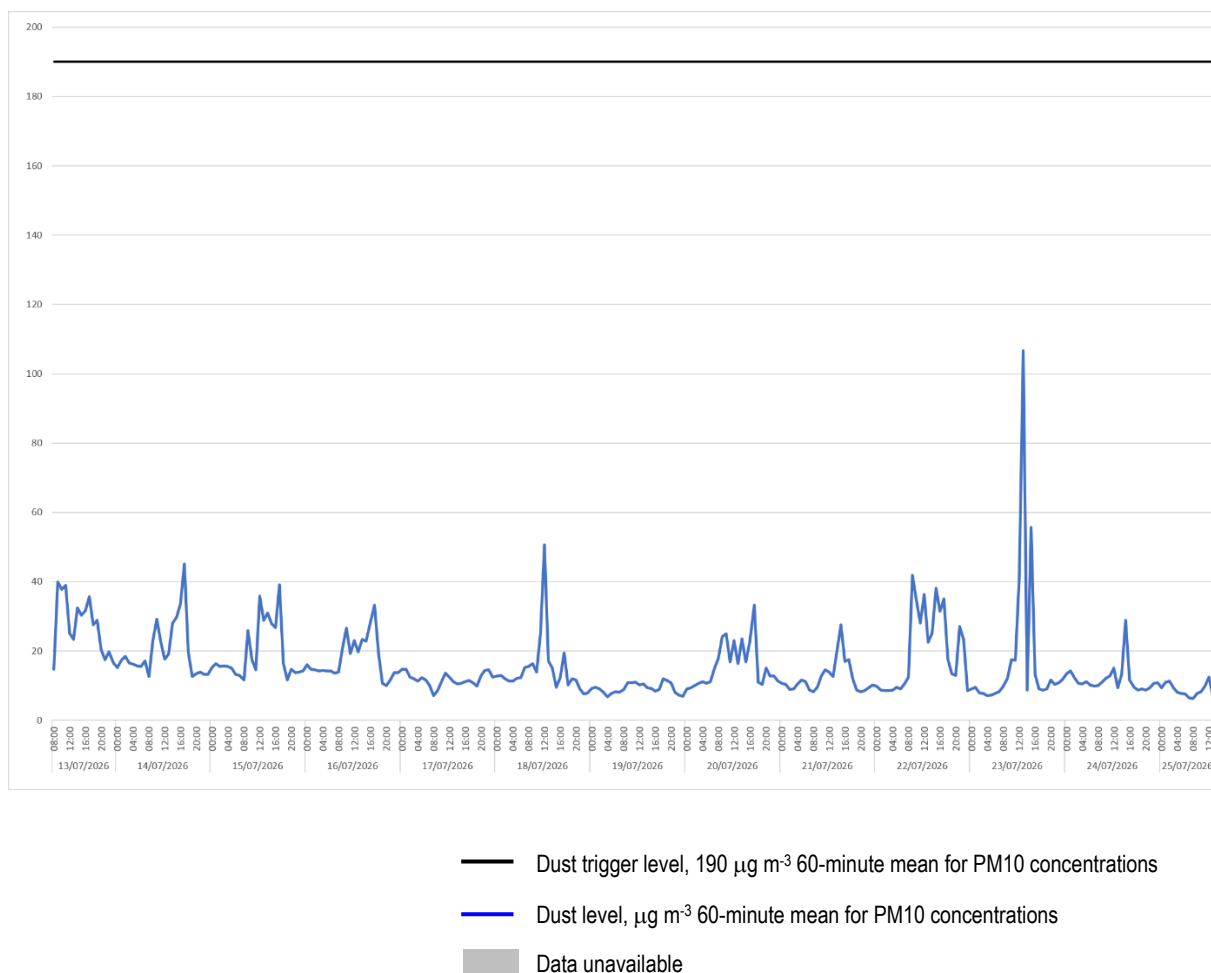

- 3.3 There was 100% data coverage of construction hours during the monitoring period. There were no exceedances of the dust trigger level of 190 $\mu\text{g m}^{-3}$ recorded at this location during construction hours.

Location 3 (meter ref. TNO4729)

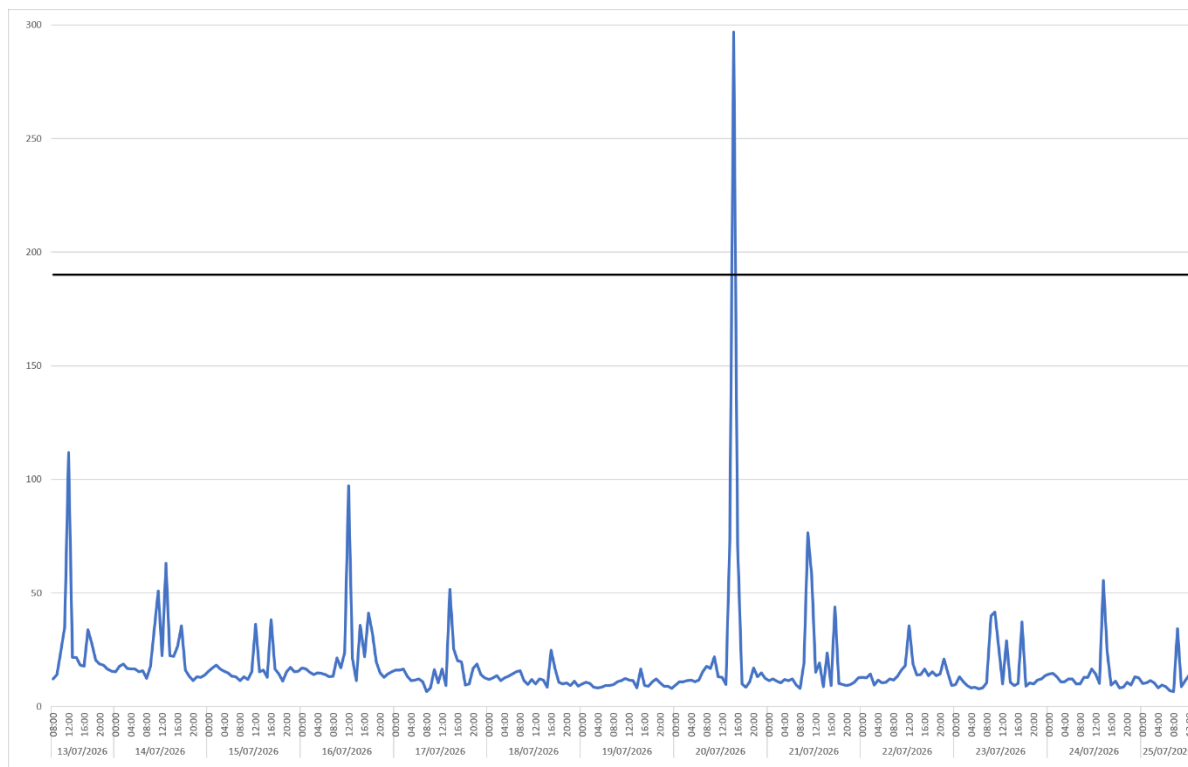

- Dust trigger level, 190 $\mu\text{g m}^{-3}$ 60-minute mean for PM10 concentrations
- Dust level, $\mu\text{g m}^{-3}$ 60-minute mean for PM10 concentrations
- Data unavailable


- 3.4 There was 100% data coverage of construction hours during the monitoring period. There was one exceedance of the dust trigger level of 190 $\mu\text{g m}^{-3}$ recorded at this location during construction hours. This occurred on Monday 20th July at 15:00 with a recorded level of 296.9 $\mu\text{g m}^{-3}$. Based on discussions with site management, this is understood to have been caused by vehicle movements within the proximity of the monitor. It is positive that no further exceedances were recorded at this location.

Noise Monitoring Results

Location 1 (meter ref. SMENK-9E5DF) – Raw Data

# Broadband Results	Date	Time	L _{Aeq} (50min)	L _{Aeq} (7hr)	L _{Aeq} (10hr)	L _{Aeq} (5hr)
	[YYYY-MM-DD]	[hh:mm:ss]	[dB]	[dB]	[dB]	[dB]
	2026-07-13	09:00:00	64.8	-	-	-
	2026-07-13	10:00:00	64.8	-	-	-
	2026-07-13	11:00:00	64.1	-	-	-
	2026-07-13	12:00:00	64.3	-	-	-
	2026-07-13	13:00:00	64.6	-	-	-
	2026-07-13	14:00:00	63.7	-	-	-
	2026-07-13	15:00:00	65.2	-	-	-
	2026-07-13	16:00:00	63.7	-	-	-
	2026-07-13	17:00:00	64.0	-	-	-
	2026-07-13	18:00:00	64.1	-	64.4	-
	2026-07-14	09:00:00	64.8	-	-	-
	2026-07-14	10:00:00	64.5	-	-	-
	2026-07-14	11:00:00	65.3	-	-	-
	2026-07-14	12:00:00	65.0	-	-	-
	2026-07-14	13:00:00	63.6	-	-	-
	2026-07-14	14:00:00	64.3	-	-	-
	2026-07-14	15:00:00	63.9	-	-	-
	2026-07-14	16:00:00	64.8	-	-	-
	2026-07-14	17:00:00	64.1	-	-	-
	2026-07-14	18:00:00	61.7	-	64.3	-
	2026-07-15	09:00:00	64.4	-	-	-
	2026-07-15	10:00:00	64.8	-	-	-
	2026-07-15	11:00:00	65.7	-	-	-
	2026-07-15	12:00:00	64.9	-	-	-
	2026-07-15	13:00:00	63.4	-	-	-
	2026-07-15	14:00:00	63.3	-	-	-
	2026-07-15	15:00:00	64.7	-	-	-
	2026-07-15	16:00:00	63.8	-	-	-
	2026-07-15	17:00:00	64.7	-	-	-
	2026-07-15	18:00:00	60.5	-	64.2	-
	2026-07-16	09:00:00	64.1	-	-	-
	2026-07-16	10:00:00	63.8	-	-	-
	2026-07-16	11:00:00	64.1	-	-	-
	2026-07-16	12:00:00	63.6	-	-	-
	2026-07-16	13:00:00	63.6	-	-	-
	2026-07-16	14:00:00	64.1	-	-	-
	2026-07-16	15:00:00	64.7	-	-	-
	2026-07-16	16:00:00	64.2	-	-	-
	2026-07-16	17:00:00	64.9	-	-	-
	2026-07-16	18:00:00	61.7	-	64.0	-
	2026-07-17	09:00:00	62.5	-	-	-
	2026-07-17	10:00:00	64.0	-	-	-
	2026-07-17	11:00:00	64.1	-	-	-
	2026-07-17	12:00:00	62.3	-	-	-
	2026-07-17	13:00:00	63.2	-	-	-
	2026-07-17	14:00:00	63.5	-	-	-
	2026-07-17	15:00:00	64.6	-	-	-
	2026-07-17	16:00:00	63.9	-	-	-
	2026-07-17	17:00:00	63.8	-	-	-
	2026-07-17	18:00:00	61.1	-	63.4	-
	2026-07-18	09:00:00	64.2	-	-	-
	2026-07-18	10:00:00	62.5	-	-	-
	2026-07-18	11:00:00	62.8	-	-	-
	2026-07-18	12:00:00	60.6	-	-	-
	2026-07-18	13:00:00	59.9	-	-	62.3
	2026-07-19	09:00:00	-	-	60.3	-
	2026-07-20	09:00:00	63.3	-	-	-
	2026-07-20	10:00:00	64.4	-	-	-
	2026-07-20	11:00:00	64.4	-	-	-
	2026-07-20	12:00:00	65.3	-	-	-
	2026-07-20	13:00:00	63.8	-	-	-
	2026-07-20	14:00:00	64.0	-	-	-
	2026-07-20	15:00:00	64.1	-	-	-
	2026-07-20	16:00:00	65.0	-	-	-
	2026-07-20	17:00:00	63.5	-	-	-
	2026-07-20	18:00:00	61.4	-	64.0	-
	2026-07-21	09:00:00	65.3	-	-	-
	2026-07-21	10:00:00	64.6	-	-	-
	2026-07-21	11:00:00	65.4	-	-	-
	2026-07-21	12:00:00	65.7	-	-	-
	2026-07-21	13:00:00	63.1	-	-	-
	2026-07-21	14:00:00	63.9	-	-	-
	2026-07-21	15:00:00	66.9	-	-	-
	2026-07-21	16:00:00	64.6	-	-	-
	2026-07-21	17:00:00	64.6	-	-	-
	2026-07-21	18:00:00	61.6	-	64.8	-
	2026-07-22	09:00:00	65.1	-	-	-
	2026-07-22	10:00:00	64.5	-	-	-
	2026-07-22	11:00:00	65.3	-	-	-
	2026-07-22	12:00:00	63.0	-	-	-
	2026-07-22	13:00:00	63.0	-	-	-
	2026-07-22	14:00:00	63.6	-	-	-
	2026-07-22	15:00:00	66.3	-	-	-
	2026-07-22	16:00:00	65.4	-	-	-
	2026-07-22	17:00:00	64.4	-	-	-
	2026-07-22	18:00:00	62.2	-	64.4	-
	2026-07-23	09:00:00	64.3	-	-	-
	2026-07-23	10:00:00	63.6	-	-	-
	2026-07-23	11:00:00	62.9	-	-	-
	2026-07-23	12:00:00	63.6	-	-	-
	2026-07-23	13:00:00	64.6	-	-	-
	2026-07-23	14:00:00	64.4	-	-	-
	2026-07-23	15:00:00	63.4	-	-	-
	2026-07-23	16:00:00	64.1	-	-	-
	2026-07-23	17:00:00	63.7	-	-	-
	2026-07-23	18:00:00	61.3	-	63.7	-
	2026-07-24	09:00:00	66.7	-	-	-
	2026-07-24	10:00:00	69.5	-	-	-
	2026-07-24	11:00:00	70.7	-	-	-
	2026-07-24	12:00:00	73.1	-	-	-
	2026-07-24	13:00:00	67.8	-	-	-
	2026-07-24	14:00:00	68.0	-	-	-
	2026-07-24	15:00:00	72.3	-	-	-
	2026-07-24	16:00:00	65.0	-	-	-
	2026-07-24	17:00:00	63.3	-	-	-
	2026-07-24	18:00:00	62.4	-	69.3	-
	2026-07-25	09:00:00	72.0	-	-	-
	2026-07-25	10:00:00	73.5	-	-	-
	2026-07-25	11:00:00	72.7	-	-	-
	2026-07-25	12:00:00	73.5	-	-	-
	2026-07-25	13:00:00	70.3	-	-	72.5

Location 1 (meter ref. SMENK-9E5DF) – Time History Data

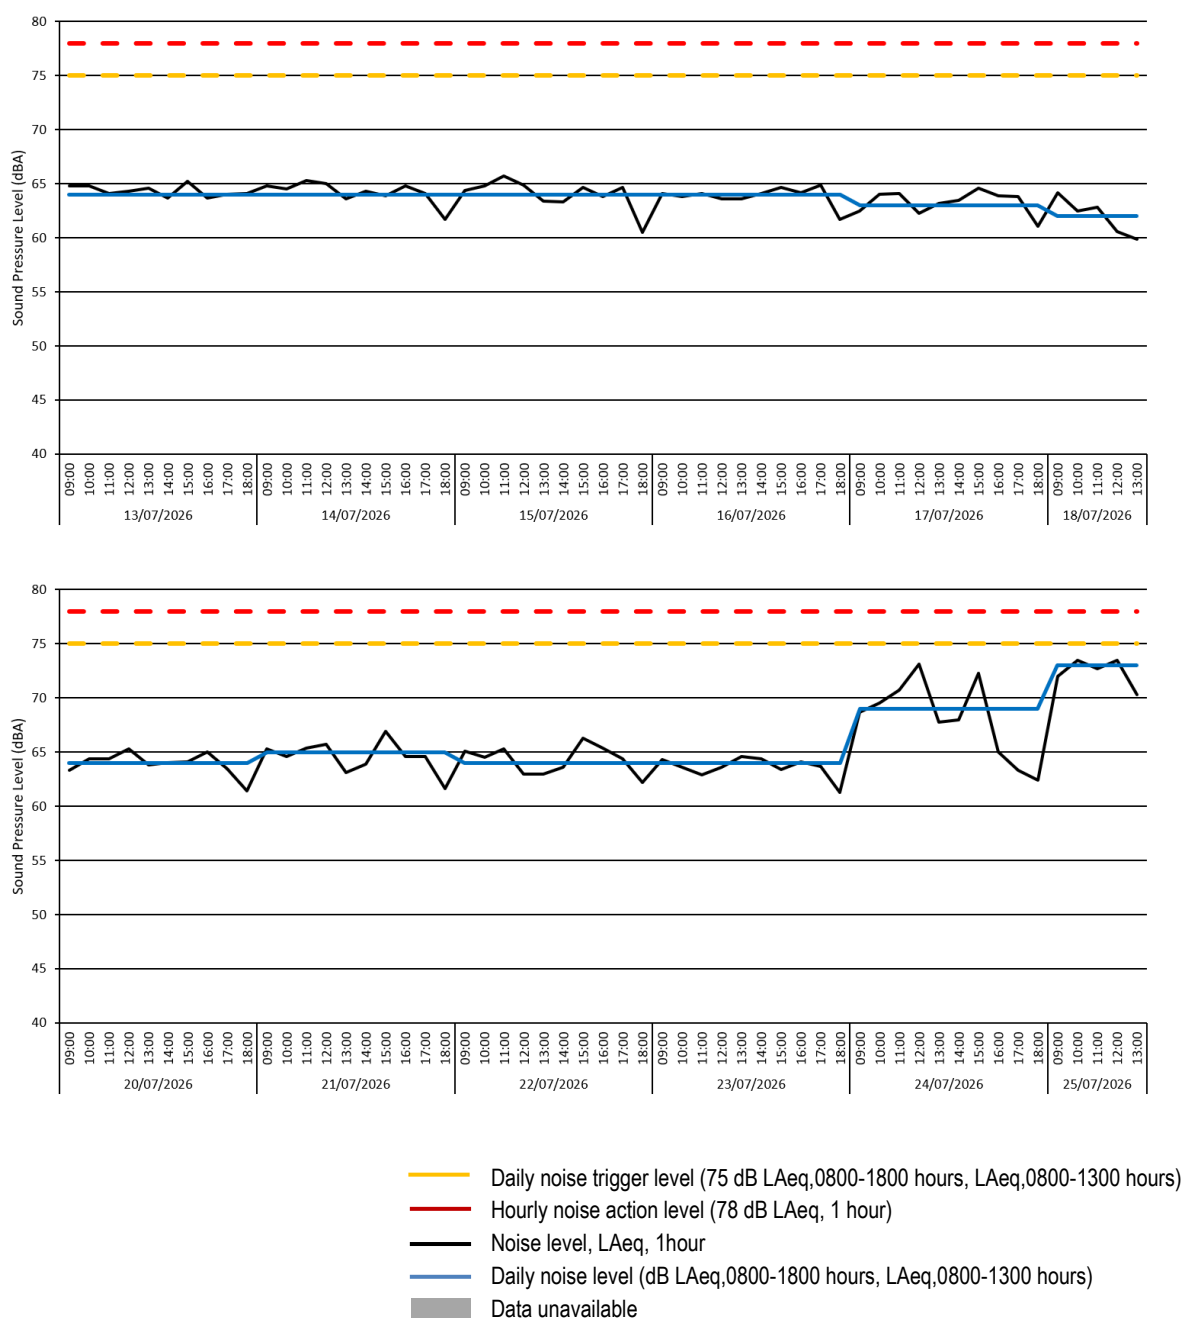


- 3.5 There was 100% data coverage at Location 1 during construction hours for the monitoring period. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq,1 hour) at this location for the monitoring period covered by this report.

Location 2 (meter ref. VFHMP-7XSY7) – Raw Data

# Broadband Results				
Date	Time	L _{Aeq} (50min)	L _{Aeq} (10hr)	L _{Aeq} (5hr)
[YYYY-MM-DD]	[hh:mm:ss]	[dB]	[dB]	[dB]
2026-07-13	09:00:00	66.6	-	-
2026-07-13	10:00:00	65.7	-	-
2026-07-13	11:00:00	62.5	-	-
2026-07-13	12:00:00	60.3	-	-
2026-07-13	13:00:00	54.8	-	-
2026-07-13	14:00:00	71.4	-	-
2026-07-13	15:00:00	69.1	-	-
2026-07-13	16:00:00	56.8	-	-
2026-07-13	17:00:00	54.9	-	-
2026-07-13	18:00:00	47.8	65.3	-
2026-07-14	09:00:00	60.3	-	-
2026-07-14	10:00:00	60.5	-	-
2026-07-14	11:00:00	56.9	-	-
2026-07-14	12:00:00	56.4	-	-
2026-07-14	13:00:00	52.1	-	-
2026-07-14	14:00:00	56.4	-	-
2026-07-14	15:00:00	58.7	-	-
2026-07-14	16:00:00	58.4	-	-
2026-07-14	17:00:00	57.0	-	-
2026-07-14	18:00:00	51.0	57.6	-
2026-07-15	09:00:00	57.0	-	-
2026-07-15	10:00:00	57.9	-	-
2026-07-15	11:00:00	56.2	-	-
2026-07-15	12:00:00	58.5	-	-
2026-07-15	13:00:00	53.8	-	-
2026-07-15	14:00:00	56.2	-	-
2026-07-15	15:00:00	57.4	-	-
2026-07-15	16:00:00	60.4	-	-
2026-07-15	17:00:00	60.6	-	-
2026-07-15	18:00:00	43.8	57.6	-
2026-07-16	09:00:00	56.7	-	-
2026-07-16	10:00:00	59.4	-	-
2026-07-16	11:00:00	57.1	-	-
2026-07-16	12:00:00	59.7	-	-
2026-07-16	13:00:00	55.9	-	-
2026-07-16	14:00:00	51.6	-	-
2026-07-16	15:00:00	55.6	-	-
2026-07-16	16:00:00	57.5	-	-
2026-07-16	17:00:00	53.4	-	-
2026-07-16	18:00:00	47.7	56.5	-
2026-07-17	09:00:00	47.6	-	-
2026-07-17	10:00:00	58.6	-	-
2026-07-17	11:00:00	60.8	-	-
2026-07-17	12:00:00	58.4	-	-
2026-07-17	13:00:00	53.7	-	-
2026-07-17	14:00:00	55.4	-	-
2026-07-17	15:00:00	60.2	-	-
2026-07-17	16:00:00	56.1	-	-
2026-07-17	17:00:00	55.2	-	-
2026-07-17	18:00:00	48.6	57.1	-
2026-07-18	09:00:00	62.5	-	-
2026-07-18	10:00:00	60.2	-	-
2026-07-18	11:00:00	60.7	-	-
2026-07-18	12:00:00	61.1	-	-
2026-07-18	13:00:00	56.7	-	60.6
2026-07-18	18:00:00	-	44.5	-
2026-07-20	09:00:00	63.0	-	-
2026-07-20	10:00:00	61.1	-	-
2026-07-20	11:00:00	61.3	-	-
2026-07-20	12:00:00	60.5	-	-
2026-07-20	13:00:00	57.5	-	-
2026-07-20	14:00:00	67.5	-	-
2026-07-20	15:00:00	60.3	-	-
2026-07-20	16:00:00	59.8	-	-
2026-07-20	17:00:00	60.0	-	-
2026-07-20	18:00:00	47.6	61.8	-
2026-07-21	09:00:00	61.6	-	-
2026-07-21	10:00:00	59.0	-	-
2026-07-21	11:00:00	60.0	-	-
2026-07-21	12:00:00	59.1	-	-
2026-07-21	13:00:00	52.9	-	-
2026-07-21	14:00:00	56.1	-	-
2026-07-21	15:00:00	58.3	-	-
2026-07-21	16:00:00	61.5	-	-
2026-07-21	17:00:00	60.1	-	-
2026-07-21	18:00:00	45.7	58.9	-
2026-07-22	09:00:00	65.0	-	-
2026-07-22	10:00:00	63.6	-	-
2026-07-22	11:00:00	67.1	-	-
2026-07-22	12:00:00	67.5	-	-
2026-07-22	13:00:00	65.8	-	-
2026-07-22	14:00:00	62.4	-	-
2026-07-22	15:00:00	66.7	-	-
2026-07-22	16:00:00	66.7	-	-
2026-07-22	17:00:00	56.6	-	-
2026-07-22	18:00:00	47.0	65.0	-
2026-07-23	09:00:00	68.0	-	-
2026-07-23	10:00:00	69.7	-	-
2026-07-23	11:00:00	69.2	-	-
2026-07-23	12:00:00	69.4	-	-
2026-07-23	13:00:00	73.2	-	-
2026-07-23	14:00:00	62.1	-	-
2026-07-23	15:00:00	67.9	-	-
2026-07-23	16:00:00	60.7	-	-
2026-07-23	17:00:00	57.0	-	-
2026-07-23	18:00:00	46.9	68.0	-
2026-07-24	09:00:00	60.5	-	-
2026-07-24	10:00:00	62.0	-	-
2026-07-24	11:00:00	58.5	-	-
2026-07-24	12:00:00	58.7	-	-
2026-07-24	13:00:00	54.2	-	-
2026-07-24	14:00:00	60.6	-	-
2026-07-24	15:00:00	57.7	-	-
2026-07-24	16:00:00	59.7	-	-
2026-07-24	17:00:00	61.1	-	-
2026-07-24	18:00:00	48.2	59.3	-
2026-07-25	09:00:00	54.1	-	-
2026-07-25	10:00:00	58.8	-	-
2026-07-25	11:00:00	55.6	-	-
2026-07-25	12:00:00	58.9	-	-
2026-07-25	13:00:00	49.5	-	56.5

Location 2 (meter ref. VFHMP-7XSY7) – Time History Data

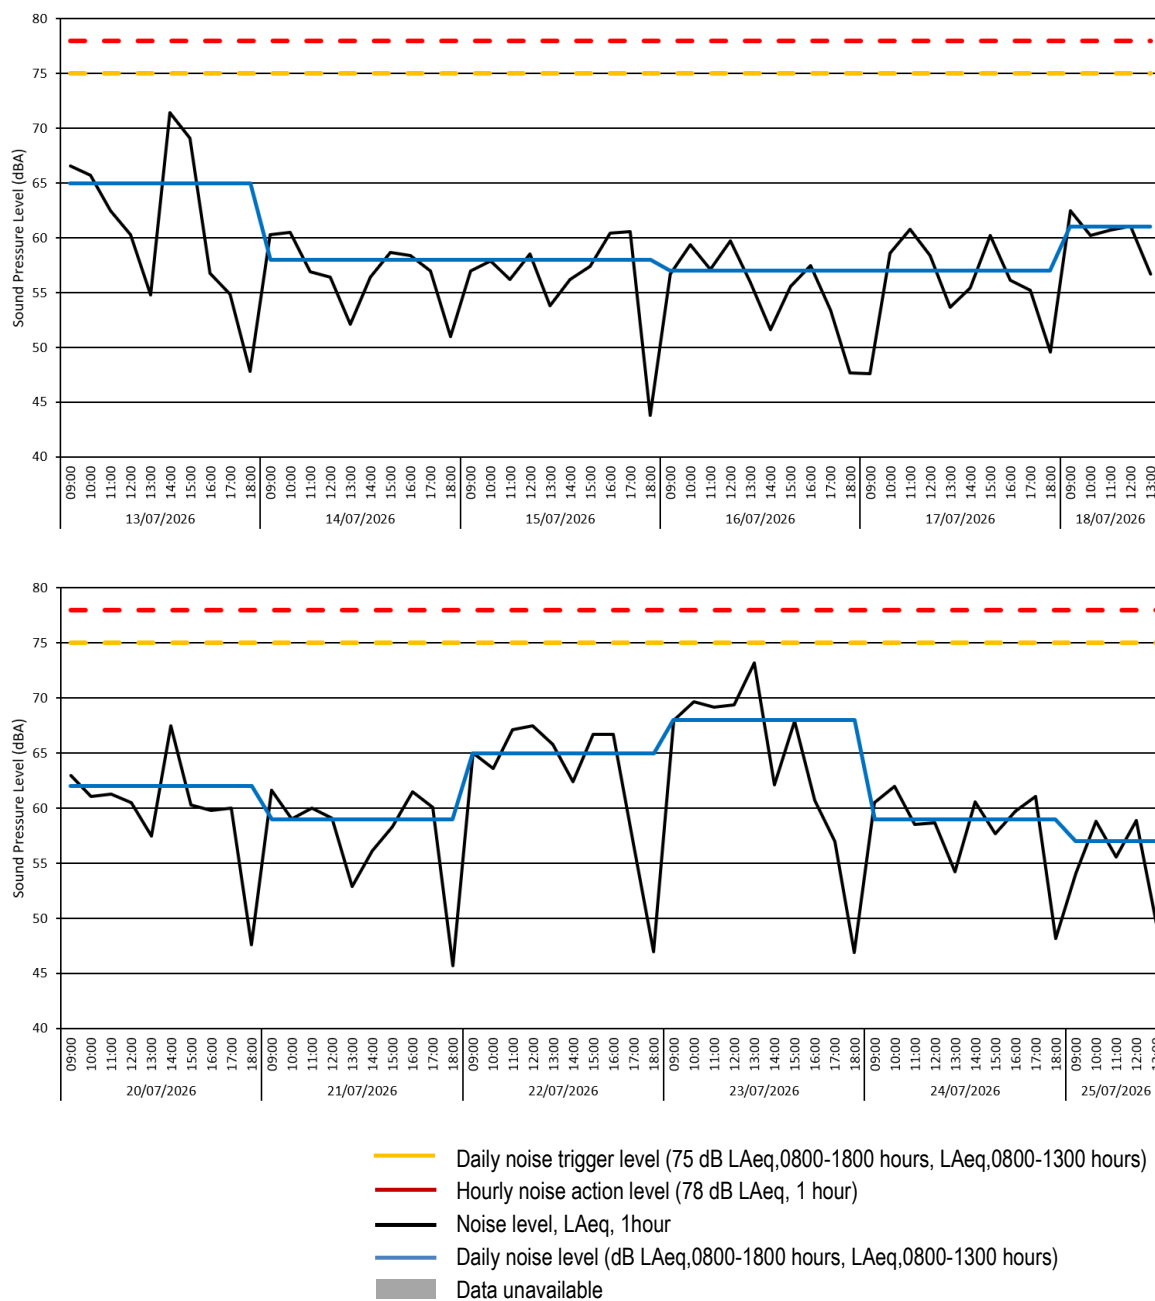


- 3.6 There was 100% data coverage at Location 2 during construction hours for the monitoring period covered by this report. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq,1 hour) at this location for the monitoring period covered by this report.

Location 3 (meter ref. P5DLY-N3J7A) – Raw Data

# Broadband Results	Date	Time	L _{eq} (60min)	L _{eq} (10hr)	L _{eq} (8hr)
	[YYYY-MM-DD]	[hh:mm:ss]	[dB]	[dB]	[dB]
	2026-07-13	09:00:00	54.7	-	-
	2026-07-13	10:00:00	60.1	-	-
	2026-07-13	11:00:00	54.6	-	-
	2026-07-13	12:00:00	56.5	-	-
	2026-07-13	13:00:00	54.6	-	-
	2026-07-13	14:00:00	51.6	-	-
	2026-07-13	15:00:00	52.2	-	-
	2026-07-13	16:00:00	52.2	-	-
	2026-07-13	17:00:00	51.6	-	-
	2026-07-13	18:00:00	52.9	55.0	-
	2026-07-14	09:00:00	57.0	-	-
	2026-07-14	10:00:00	56.9	-	-
	2026-07-14	11:00:00	56.2	-	-
	2026-07-14	12:00:00	55.3	-	-
	2026-07-14	13:00:00	55.0	-	-
	2026-07-14	14:00:00	54.2	-	-
	2026-07-14	15:00:00	54.3	-	-
	2026-07-14	16:00:00	53.6	-	-
	2026-07-14	17:00:00	55.0	-	-
	2026-07-14	18:00:00	46.2	55.0	-
	2026-07-15	09:00:00	55.2	-	-
	2026-07-15	10:00:00	54.1	-	-
	2026-07-15	11:00:00	55.9	-	-
	2026-07-15	12:00:00	55.6	-	-
	2026-07-15	13:00:00	52.3	-	-
	2026-07-15	14:00:00	53.0	-	-
	2026-07-15	15:00:00	52.7	-	-
	2026-07-15	16:00:00	57.2	-	-
	2026-07-15	17:00:00	53.0	-	-
	2026-07-15	18:00:00	44.5	54.2	-
	2026-07-16	09:00:00	56.2	-	-
	2026-07-16	10:00:00	56.0	-	-
	2026-07-16	11:00:00	56.7	-	-
	2026-07-16	12:00:00	56.7	-	-
	2026-07-16	13:00:00	53.6	-	-
	2026-07-16	14:00:00	52.1	-	-
	2026-07-16	15:00:00	53.5	-	-
	2026-07-16	16:00:00	52.2	-	-
	2026-07-16	17:00:00	55.5	-	-
	2026-07-16	18:00:00	47.1	54.7	-
	2026-07-17	09:00:00	45.9	-	-
	2026-07-17	10:00:00	56.0	-	-
	2026-07-17	11:00:00	53.0	-	-
	2026-07-17	12:00:00	56.1	-	-
	2026-07-17	13:00:00	51.4	-	-
	2026-07-17	14:00:00	54.5	-	-
	2026-07-17	15:00:00	53.8	-	-
	2026-07-17	16:00:00	53.6	-	-
	2026-07-17	17:00:00	55.0	-	-
	2026-07-17	18:00:00	46.4	53.6	-
	2026-07-18	09:00:00	48.6	-	-
	2026-07-18	10:00:00	48.7	-	-
	2026-07-18	11:00:00	54.3	-	-
	2026-07-18	12:00:00	48.9	-	-
	2026-07-18	13:00:00	52.6	-	51.6
	2026-07-19	18:00:00	-	49.1	-
	2026-07-20	09:00:00	54.8	-	-
	2026-07-20	10:00:00	56.6	-	-
	2026-07-20	11:00:00	52.1	-	-
	2026-07-20	12:00:00	54.2	-	-
	2026-07-20	13:00:00	51.2	-	-
	2026-07-20	14:00:00	63.2	-	-
	2026-07-20	15:00:00	67.1	-	-
	2026-07-20	16:00:00	58.4	-	-
	2026-07-20	17:00:00	52.8	-	-
	2026-07-20	18:00:00	44.9	59.8	-
	2026-07-21	09:00:00	57.1	-	-
	2026-07-21	10:00:00	64.0	-	-
	2026-07-21	11:00:00	62.5	-	-
	2026-07-21	12:00:00	61.6	-	-
	2026-07-21	13:00:00	60.3	-	-
	2026-07-21	14:00:00	53.0	-	-
	2026-07-21	15:00:00	53.9	-	-
	2026-07-21	16:00:00	53.9	-	-
	2026-07-21	17:00:00	59.7	-	-
	2026-07-21	18:00:00	45.3	59.5	-
	2026-07-22	09:00:00	56.1	-	-
	2026-07-22	10:00:00	55.8	-	-
	2026-07-22	11:00:00	55.3	-	-
	2026-07-22	12:00:00	60.6	-	-
	2026-07-22	13:00:00	53.4	-	-
	2026-07-22	14:00:00	55.1	-	-
	2026-07-22	15:00:00	55.6	-	-
	2026-07-22	16:00:00	54.5	-	-
	2026-07-22	17:00:00	55.8	-	-
	2026-07-22	18:00:00	48.9	55.9	-
	2026-07-23	09:00:00	59.7	-	-
	2026-07-23	10:00:00	58.2	-	-
	2026-07-23	11:00:00	55.6	-	-
	2026-07-23	12:00:00	54.5	-	-
	2026-07-23	13:00:00	56.5	-	-
	2026-07-23	14:00:00	58.3	-	-
	2026-07-23	15:00:00	56.1	-	-
	2026-07-23	16:00:00	53.6	-	-
	2026-07-23	17:00:00	62.7	-	-
	2026-07-23	18:00:00	47.6	57.7	-
	2026-07-24	09:00:00	55.2	-	-
	2026-07-24	10:00:00	54.5	-	-
	2026-07-24	11:00:00	54.2	-	-
	2026-07-24	12:00:00	53.3	-	-
	2026-07-24	13:00:00	50.8	-	-
	2026-07-24	14:00:00	54.7	-	-
	2026-07-24	15:00:00	53.7	-	-
	2026-07-24	16:00:00	52.7	-	-
	2026-07-24	17:00:00	55.8	-	-
	2026-07-24	18:00:00	48.7	53.8	-
	2026-07-25	09:00:00	57.6	-	-
	2026-07-25	10:00:00	48.9	-	-
	2026-07-25	11:00:00	50.7	-	-
	2026-07-25	12:00:00	48.2	-	-
	2026-07-25	13:00:00	48.1	-	52.8

Location 3 (meter ref. P5DLY-N3J7A) – Time History Graph

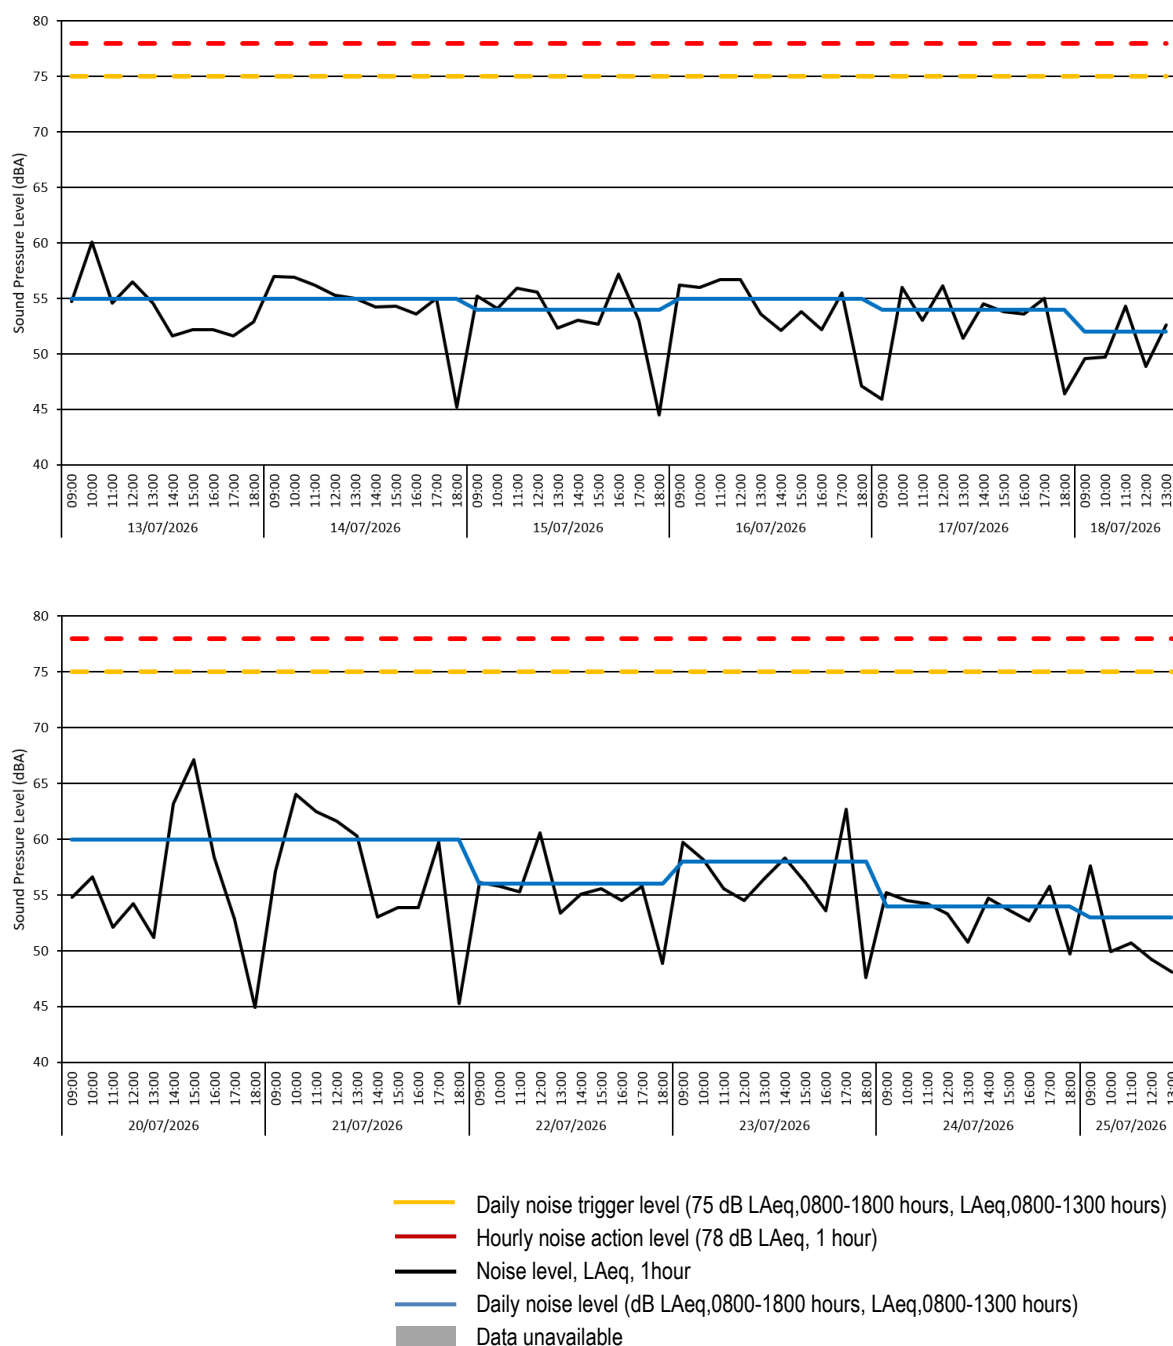

3.7 There was 100% data coverage at Location 3 during construction hours for the monitoring period covered by this report. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq,1 hour) at this location for the monitoring period covered by this report.


Vibration Monitoring Results

Location 1 (meter ref. PIJIVI) – Raw Data

Measuring point: Holloway - L1
Period: 13/07/26 - 25/07/26
Criteria mm/s PPV 1.0
Exceedances 0

Order	Value	Date	Time
1	0.77	16/07/2026	12:58
2	0.48	21/07/2026	13:45
3	0.48	16/07/2026	15:17
4	0.44	16/07/2026	09:35
5	0.43	20/07/2026	14:58
6	0.41	16/07/2026	09:44
7	0.39	21/07/2026	15:28
8	0.38	13/07/2026	16:50
9	0.38	15/07/2026	15:16
10	0.33	16/07/2026	08:49

Location 1 (meter ref. PIJIVI) – Time-history graph

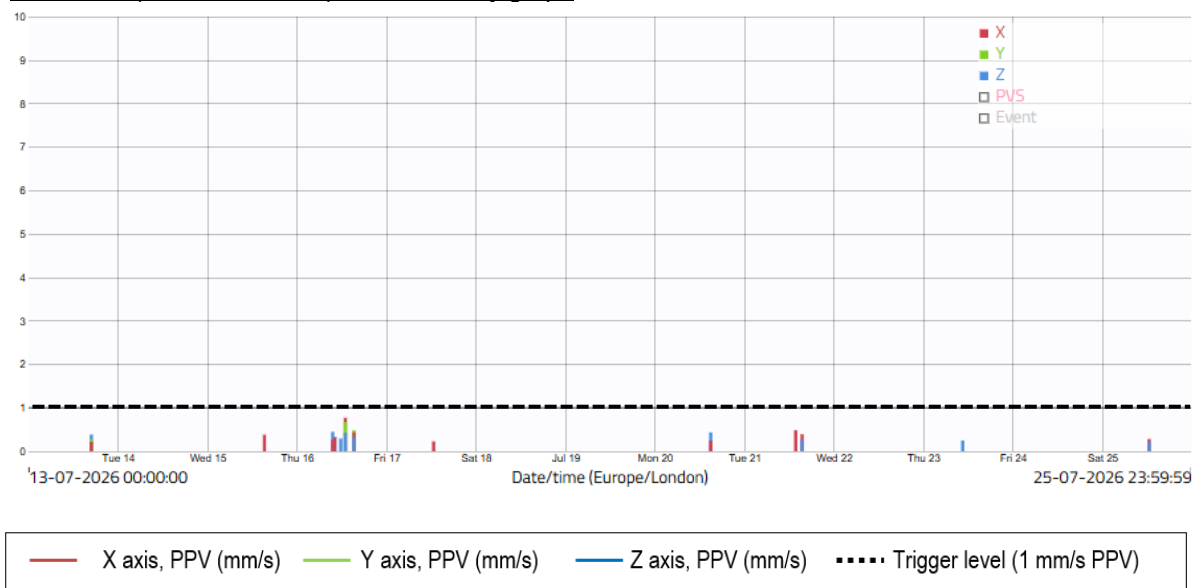

- 3.8 There was 100% data coverage at Location 1 during construction hours for the monitoring period covered by this report. There were no exceedances of the project vibration trigger level of 1.0 mm/s PPV.


Location 2 (meter ref. LEQUMO) – Raw data

Measuring point: Holloway - L2
Period: 13/07/26 - 25/07/26

Criteria mm/s PPV: 1.0
Exceedances: 2

Order	Value	Date	Time
1	1.30	20/07/2026	10:21
2	1.25	22/07/2026	14:46
3	1.00	13/07/2026	14:52
4	0.79	23/07/2026	09:58
5	0.66	23/07/2026	14:11
6	0.62	23/07/2026	11:13
7	0.58	24/07/2026	09:42
8	0.56	23/07/2026	11:12
9	0.54	13/07/2026	13:49
10	0.53	20/07/2026	13:45

Location 2 (meter ref. LEQUMO) – Time-history graph

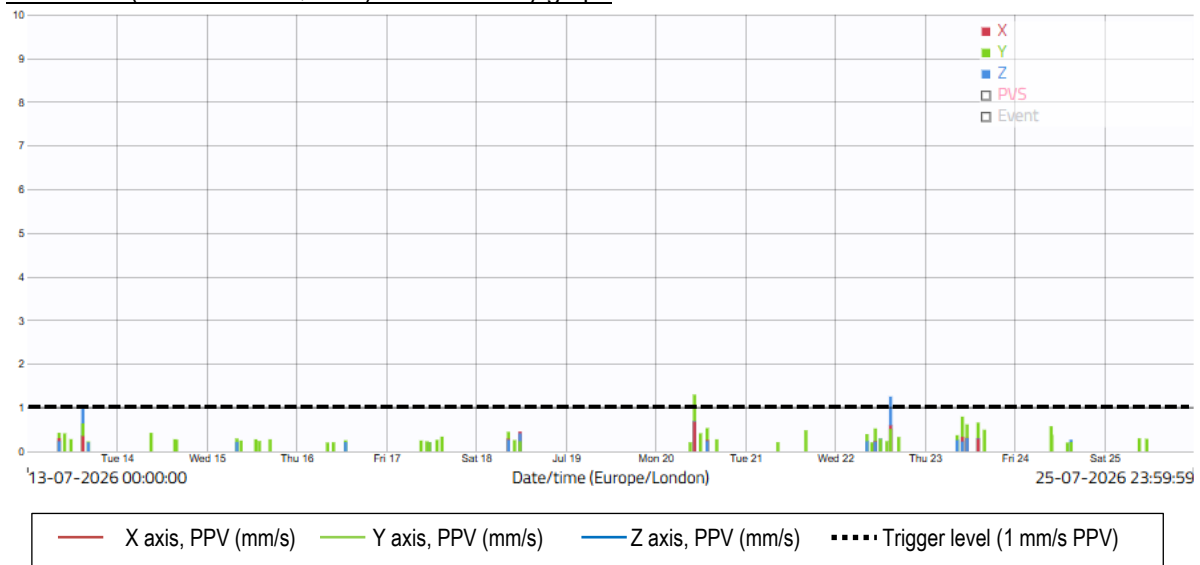

- 3.9 There was 100% data coverage at Location 2 during construction hours for the monitoring period covered by this report. There were two exceedances of the project vibration trigger level of 1.0 mm/s PPV. The highest recorded level occurred on Monday 20th July at 10:21, with a recorded level of 1.3 mm/s PPV. Based on discussions with site management, the exceedances are understood to have been caused by the brickwork taking place at Block E.

Location 3 (meter ref. RIYORU) – Raw Data

Measuring point:
 Holloway - L3


Criteria mm/s PPV
 4.0

Period:
 13/07/26 - 25/07/26

Exceedances
 0

Order	Value	Date	Time
1	1.84	13/07/2026	15:20
2	1.16	21/07/2026	10:01
3	1.00	20/07/2026	14:51
4	0.97	21/07/2026	10:00
5	0.91	21/07/2026	10:03
6	0.89	21/07/2026	10:05
7	0.80	21/07/2026	09:55
8	0.79	21/07/2026	09:59
9	0.77	20/07/2026	13:47
10	0.72	21/07/2026	09:52

Location 3 (meter ref. RIYORU) – Time-history graph

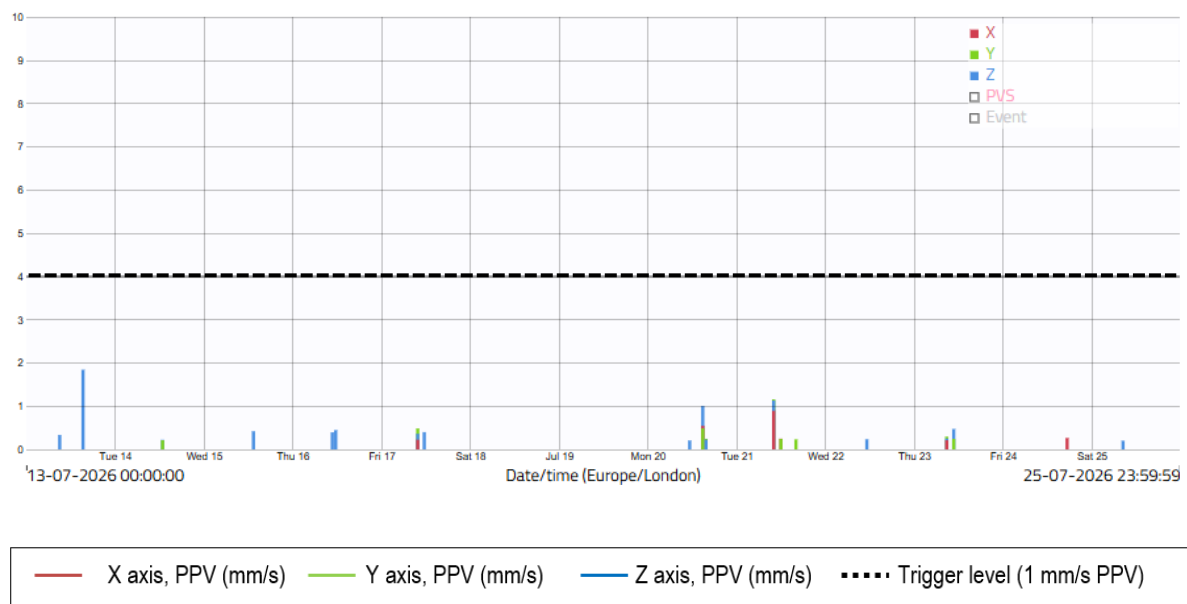

- 3.10 There was 100% data coverage at Location 3 during construction hours for the monitoring period. There were no exceedances of the project vibration trigger level of 4.0 mm/s PPV.


Location 4 (meter ref. TEJELU) – Raw data

Measuring point: Period:
Holloway - L4 23/07/26 - 25/07/26

Criteria mm/s PPV Exceedances
1.0 0

Order	Value	Date	Time
1	0.30	24/07/2026	12:32
2	0.28	25/07/2026	09:51
3	0.25	25/07/2026	09:22
4	0.25	24/07/2026	09:55
5	0.22	24/07/2026	10:30
6	0.00	23/07/2026	08:53
7	0.00	23/07/2026	08:53
8	0.00	23/07/2026	08:53
9	0.00	23/07/2026	08:53
10	0.00	23/07/2026	08:53

Location 4 (meter ref. TEJELU) – Time-history graph

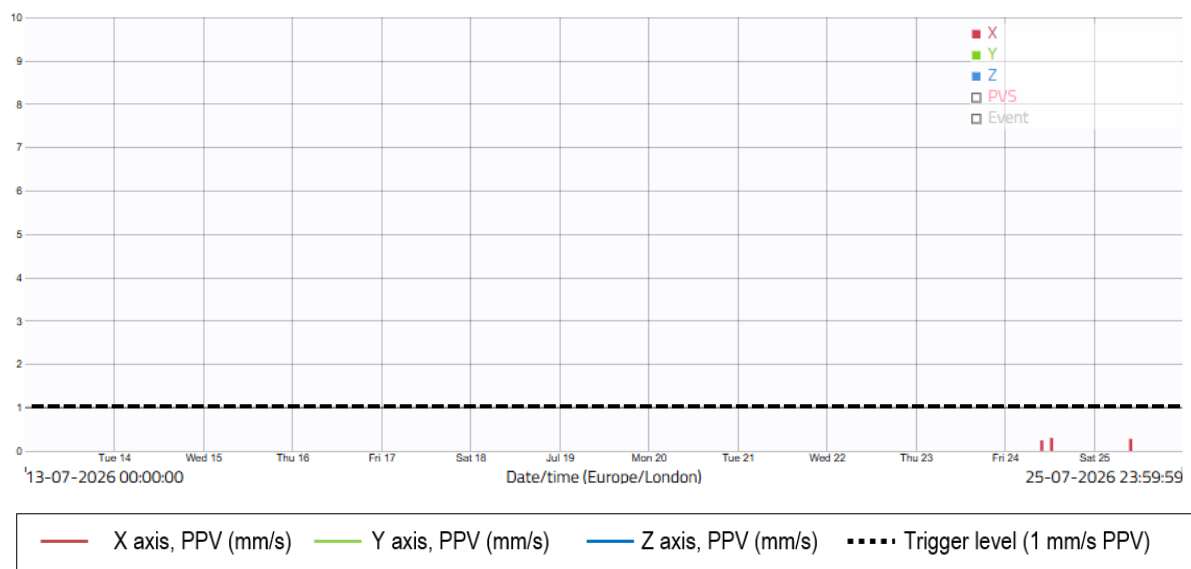

- 3.11 There was 23% data coverage at Location 4 during construction hours for the monitoring period covered by this report due to a drained battery from Friday 10th July at 08:06 AM. The battery has since been changed and data collection has resumed. From the available data, there were no exceedances of the project vibration trigger level of 1.0 mm/s PPV at Location 4 during construction hours for the monitoring period covered by this report.
