

Holloway Park, London

Construction Monitoring Report

Client: London Square
Ref: CM140-22405-R0
Date: 7 September 2026
Note by: George Spence, BSc (Hons) , Acoustics Consultant
Reviewed by: Anthony Coraci, MSc DipIOA, Senior Acoustics Consultant

1. INTRODUCTION

- 1.1 This Technical Note sets out results of the construction monitoring being carried out at the above site between Monday 10 August & Saturday 22 August 2026. The monitoring is being carried out in general agreement with the methodology in the current Section 61 Consent between the London Borough of Islington and London Square.

2. SITE ACTIVITIES

- 2.1 The following activities have been carried during the period covered by this report, in addition to the usual use of the Haul Road with site vehicles, and mobile plant used around the site:


- Fixing works and brickwork at Blocks C, D, E1 & E2.
- Block E window installations.
- Brickwork and internal fitout across Blocks C1, D1, D2, D3, all E blocks

3. MONITORING DATA

- 3.1 This section sets out a summary of the monitoring data that has been recorded onsite and provides a discussion of any exceedances and best practicable means incorporated by the site team if exceedances were believed to be construction related.


Dust Monitoring Results

Location 1 (meter ref. TNO3599)

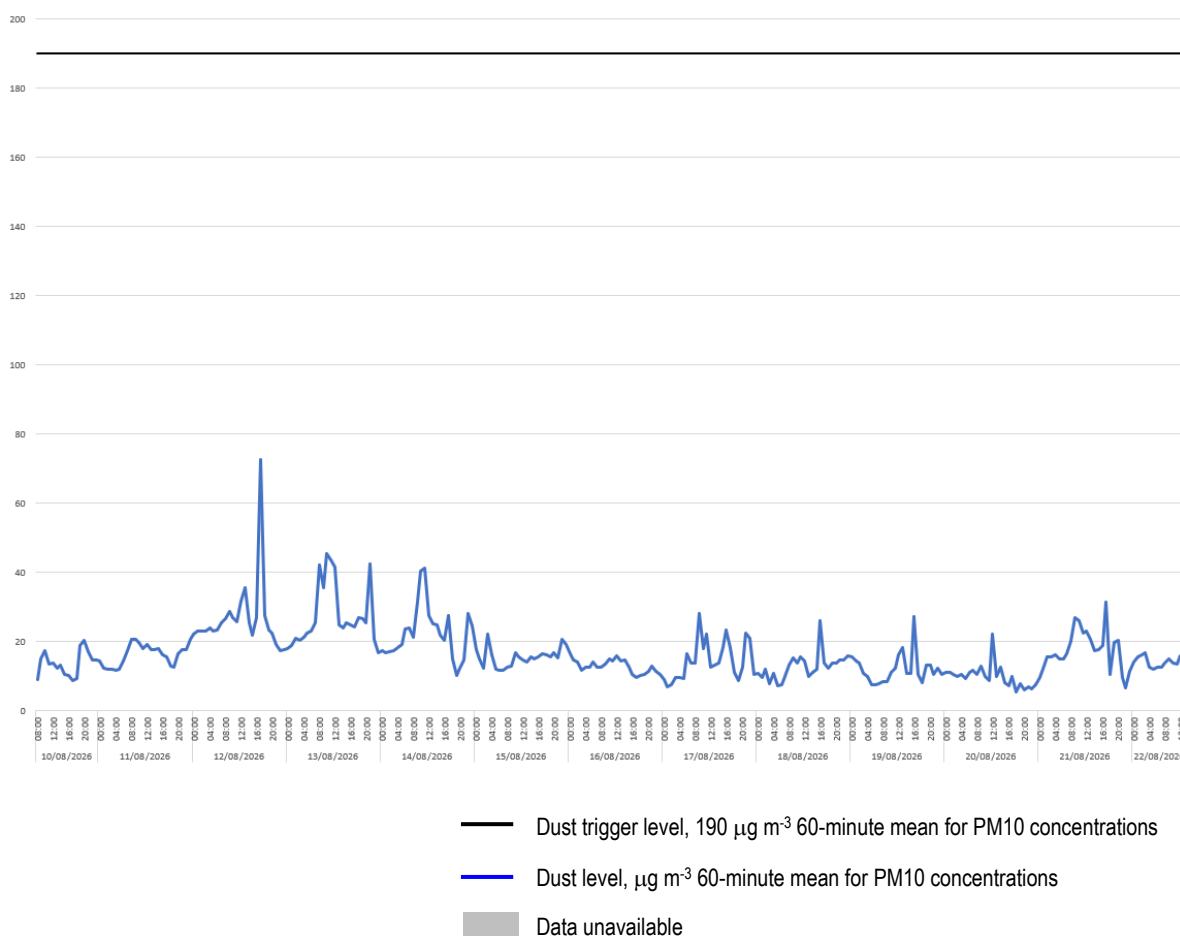


- 3.2 There was 100% data coverage during the monitoring period. There were no exceedances of the dust trigger level of 190 $\mu\text{g m}^{-3}$ recorded at this location during construction hours.

Location 2 (meter ref. TNO4719)

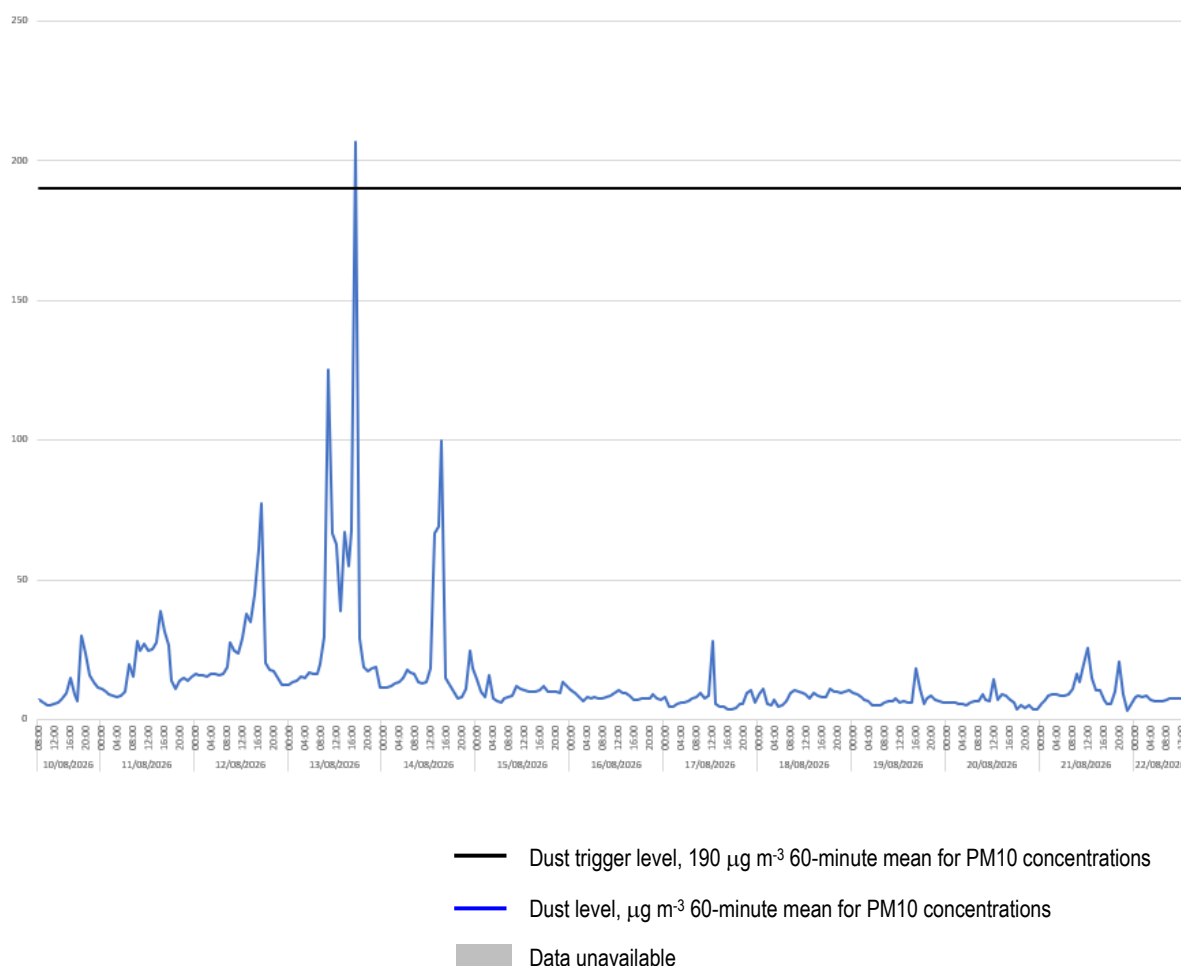

- 3.3 There was 100% data coverage of construction hours during the monitoring period. There was one exceedance of the dust trigger level of 190 $\mu\text{g m}^{-3}$ at this location during construction hours, which occurred at 17:00 on Thursday 13 August, with a recorded level of 206.8 $\mu\text{g m}^{-3}$. Based on discussions with site management, this is understood to have been caused by fixing works taking place at Block E.

Location 3 (meter ref. TNO4729)

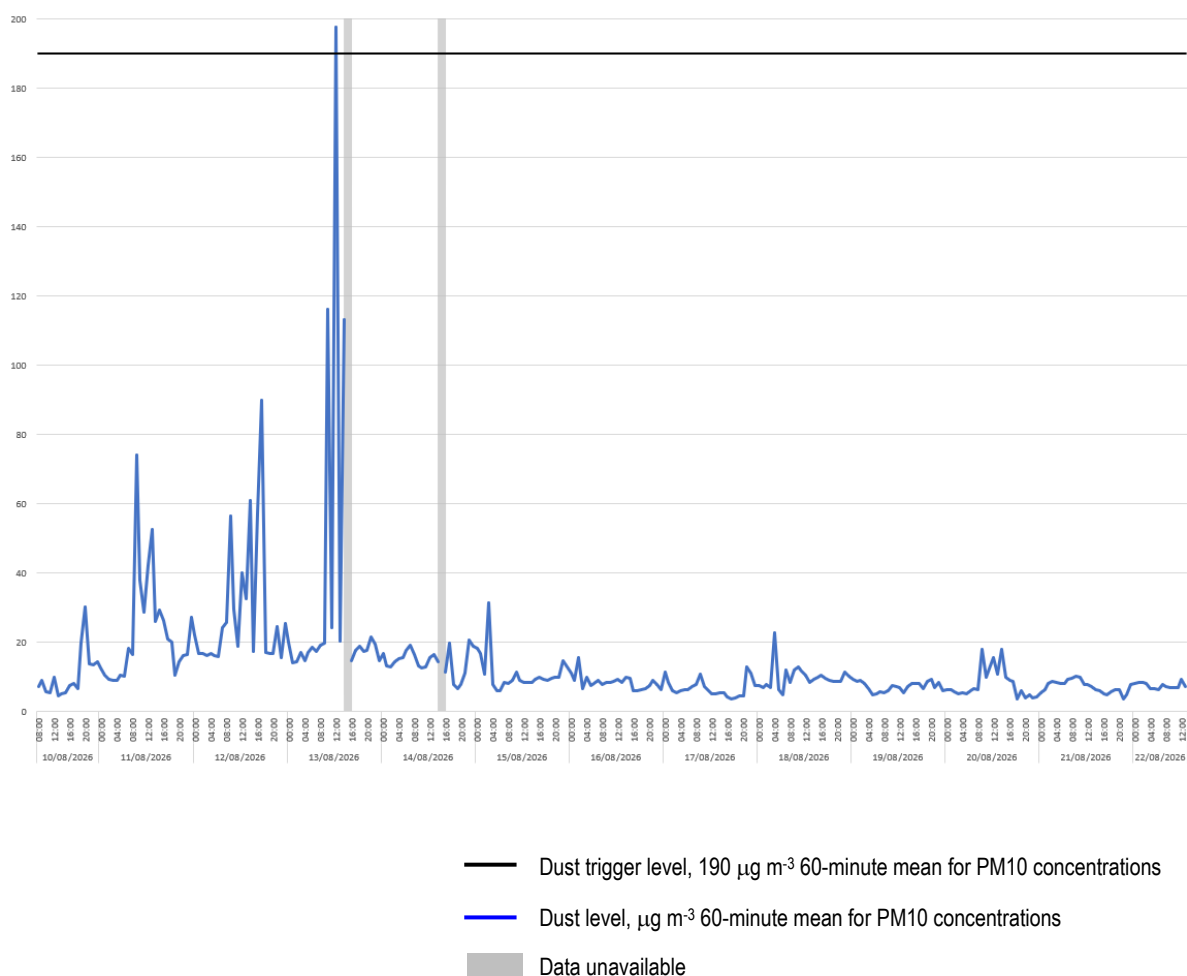


- 3.4 There was 98% data coverage of construction hours during the monitoring period due to short-lived power outages on Thursday 13 and Friday 14 August. There was one exceedance of the dust trigger level of 190 $\mu\text{g m}^{-3}$ at this location during construction hours, which occurred at 12:00 on Thursday 13 August, with a recorded level of 197.7 $\mu\text{g m}^{-3}$. This is understood to have been caused by site vehicle movements within the vicinity of the monitor.

Noise Monitoring Results

Location 1 (meter ref. SMENK-9E5DF) – Raw Data

# Broadband Results					
Date	Time	L _{Aeq} (5Min)	L _{Aeq} (7hr)	L _{Aeq} (10hr)	L _{Aeq} (2hr)
[YYYY-MM-DD]	[HH:mm:ss]	[dB]	[dB]	[dB]	[dB]
2025-08-10	09:00:00	64.4	---	---	---
2025-08-10	10:00:00	65.5	---	---	---
2025-08-10	11:00:00	65.2	---	---	---
2025-08-10	12:00:00	65.2	---	---	---
2025-08-10	13:00:00	62.1	---	---	---
2025-08-10	14:00:00	63.2	---	---	---
2025-08-10	15:00:00	64.6	---	---	---
2025-08-10	16:00:00	64.6	---	---	---
2025-08-10	17:00:00	64.2	---	---	---
2025-08-10	18:00:00	61.4	---	64.2	---
2025-08-11	09:00:00	65.4	---	---	---
2025-08-11	10:00:00	64.6	---	---	---
2025-08-11	11:00:00	64.5	---	---	---
2025-08-11	12:00:00	64.6	---	---	---
2025-08-11	13:00:00	63.4	---	---	---
2025-08-11	14:00:00	66.2	---	---	---
2025-08-11	15:00:00	64.9	---	---	---
2025-08-11	16:00:00	65.6	---	---	---
2025-08-11	17:00:00	63.9	---	---	---
2025-08-11	18:00:00	62.6	---	64.7	---
2025-08-12	09:00:00	66.3	---	---	---
2025-08-12	10:00:00	65.1	---	---	---
2025-08-12	11:00:00	63.2	---	---	---
2025-08-12	12:00:00	64.1	---	---	---
2025-08-12	13:00:00	65.6	---	---	---
2025-08-12	14:00:00	64.6	---	---	---
2025-08-12	15:00:00	64.7	---	---	---
2025-08-12	16:00:00	63.2	---	---	---
2025-08-12	17:00:00	61.7	---	---	---
2025-08-12	18:00:00	62.3	---	64.3	---
2025-08-13	09:00:00	64.1	---	---	---
2025-08-13	10:00:00	64.6	---	---	---
2025-08-13	11:00:00	62.8	---	---	---
2025-08-13	12:00:00	62.6	---	---	---
2025-08-13	13:00:00	62.7	---	---	---
2025-08-13	14:00:00	63.7	---	---	---
2025-08-13	15:00:00	64.1	---	---	---
2025-08-13	16:00:00	63.9	---	---	---
2025-08-13	17:00:00	62.0	---	---	---
2025-08-13	18:00:00	62.3	---	63.4	---
2025-08-14	09:00:00	64.2	---	---	---
2025-08-14	10:00:00	64.6	---	---	---
2025-08-14	11:00:00	62.6	---	---	---
2025-08-14	12:00:00	63.7	---	---	---
2025-08-14	13:00:00	64.8	---	---	---
2025-08-14	14:00:00	64.0	---	---	---
2025-08-14	15:00:00	62.1	---	---	---
2025-08-14	16:00:00	62.1	---	---	---
2025-08-14	17:00:00	61.7	---	---	---
2025-08-14	18:00:00	60.3	---	63.2	---
2025-08-15	09:00:00	60.9	---	---	---
2025-08-15	10:00:00	59.5	---	---	---
2025-08-15	11:00:00	61.0	---	---	---
2025-08-15	12:00:00	61.8	---	---	---
2025-08-15	13:00:00	61.5	---	---	61.0
2025-08-16	18:00:00	---	---	60.1	---
2025-08-17	09:00:00	67.2	---	---	---
2025-08-17	10:00:00	62.3	---	---	---
2025-08-17	11:00:00	63.3	---	---	---
2025-08-17	12:00:00	63.1	---	---	---
2025-08-17	13:00:00	63.0	---	---	---
2025-08-17	14:00:00	63.0	---	---	---
2025-08-17	15:00:00	63.2	---	---	---
2025-08-17	16:00:00	64.4	---	---	---
2025-08-17	17:00:00	62.5	---	---	---
2025-08-17	18:00:00	61.3	---	63.7	---
2025-08-18	09:00:00	64.3	---	---	---
2025-08-18	10:00:00	64.2	---	---	---
2025-08-18	11:00:00	62.9	---	---	---
2025-08-18	12:00:00	64.6	---	---	---
2025-08-18	13:00:00	63.2	---	---	---
2025-08-18	14:00:00	64.6	---	---	---
2025-08-18	15:00:00	64.6	---	---	---
2025-08-18	16:00:00	64.1	---	---	---
2025-08-18	17:00:00	66.2	---	---	---
2025-08-18	18:00:00	62.9	---	64.9	---
2025-08-19	09:00:00	65.8	---	---	---
2025-08-19	10:00:00	64.2	---	---	---
2025-08-19	11:00:00	66.0	---	---	---
2025-08-19	12:00:00	67.7	---	---	---
2025-08-19	13:00:00	63.8	---	---	---
2025-08-19	14:00:00	63.7	---	---	---
2025-08-19	15:00:00	62.6	---	---	---
2025-08-19	16:00:00	63.0	---	---	---
2025-08-19	17:00:00	65.7	---	---	---
2025-08-19	18:00:00	62.1	---	64.8	---
2025-08-20	09:00:00	67.6	---	---	---
2025-08-20	10:00:00	66.5	---	---	---
2025-08-20	11:00:00	64.9	---	---	---
2025-08-20	12:00:00	64.8	---	---	---
2025-08-20	13:00:00	63.6	---	---	---
2025-08-20	14:00:00	64.0	---	---	---
2025-08-20	15:00:00	63.7	---	---	---
2025-08-20	16:00:00	64.5	---	---	---
2025-08-20	17:00:00	65.6	---	---	---
2025-08-20	18:00:00	60.7	---	64.9	---
2025-08-21	09:00:00	64.5	---	---	---
2025-08-21	10:00:00	64.2	---	---	---
2025-08-21	11:00:00	64.0	---	---	---
2025-08-21	12:00:00	64.4	---	---	---
2025-08-21	13:00:00	65.8	---	---	---
2025-08-21	14:00:00	63.6	---	---	---
2025-08-21	15:00:00	67.1	---	---	---
2025-08-21	16:00:00	67.0	---	---	---
2025-08-21	17:00:00	62.8	---	---	---
2025-08-21	18:00:00	62.2	---	64.8	---
2025-08-22	09:00:00	68.8	---	---	---
2025-08-22	10:00:00	61.4	---	---	---
2025-08-22	11:00:00	62.4	---	---	---
2025-08-22	12:00:00	61.0	---	---	---
2025-08-22	13:00:00	59.7	---	---	61.1

Location 1 (meter ref. SMENK-9E5DF) – Time History Data

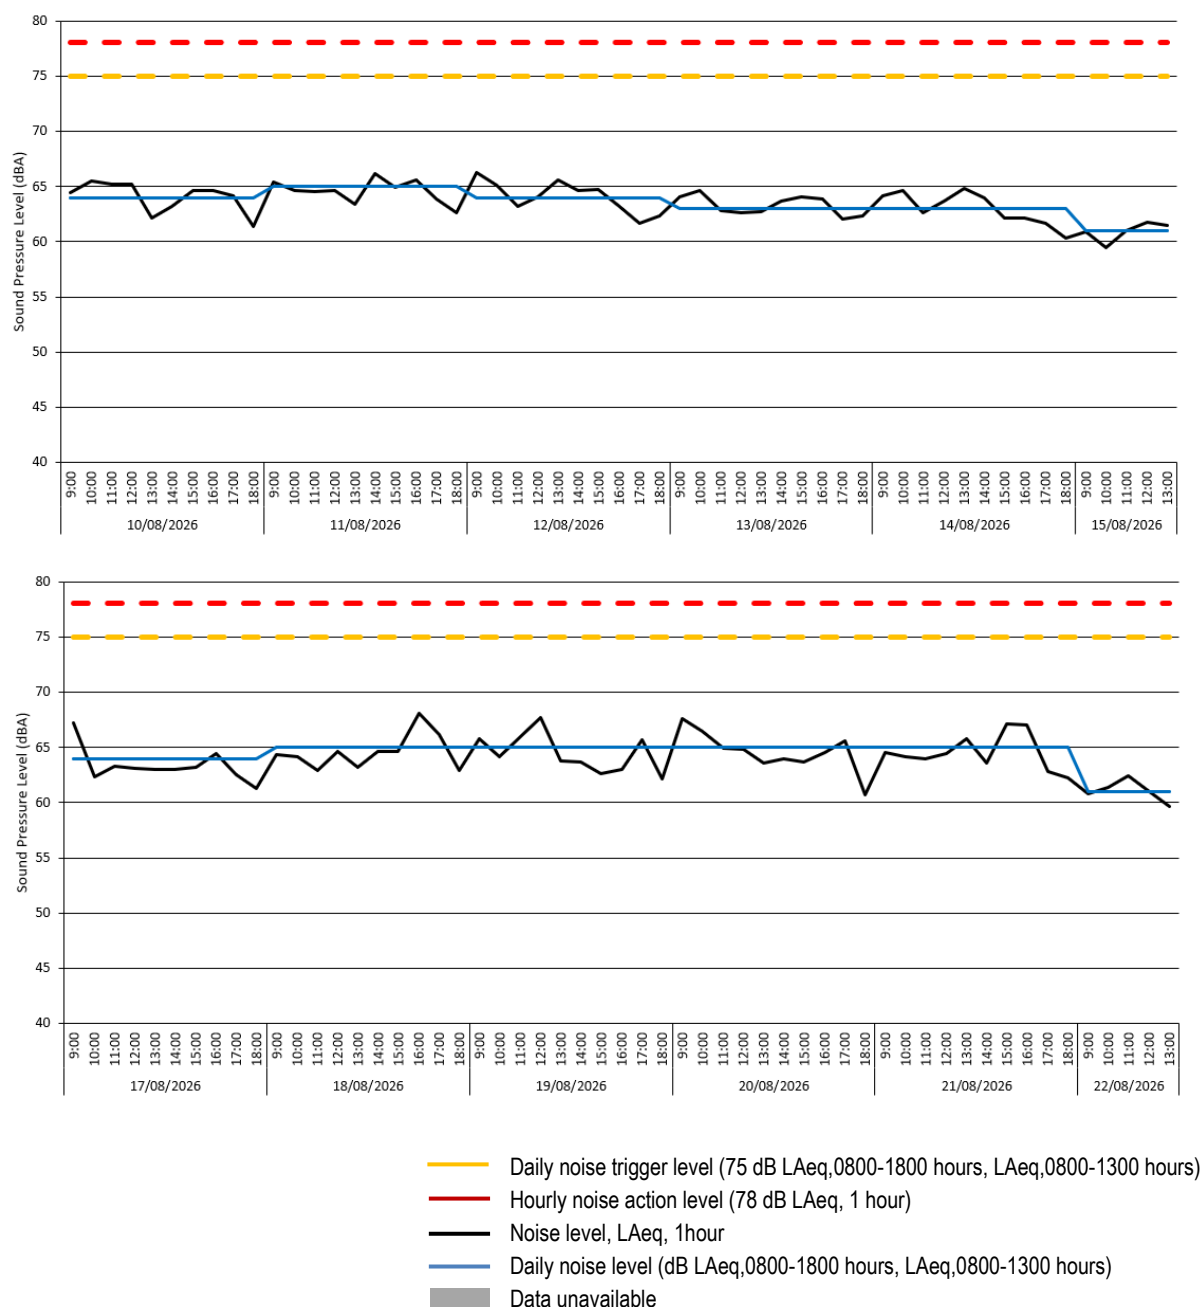


- 3.5 There was 100% data coverage at Location 1 during construction hours for the monitoring period. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq, 1 hour) at this location for the monitoring period covered by this report.

Location 2 (meter ref. VFHMP-7XSY7) – Raw Data

# Broadband Results	Date	Time	L[Aeq](50min)	L[Aeq](10hr)	L[Aeq](5hr)
	[YYYY-MM-DD]	[hh:mm:ss]	[dB]	[dB]	[dB]
	2025-08-10	09:00:00	60.5	---	---
	2025-08-10	10:00:00	61.8	---	---
	2025-08-10	11:00:00	59.3	---	---
	2025-08-10	12:00:00	62.1	---	---
	2025-08-10	13:00:00	56.7	---	---
	2025-08-10	14:00:00	57.2	---	---
	2025-08-10	15:00:00	61.3	---	---
	2025-08-10	16:00:00	56.5	---	---
	2025-08-10	17:00:00	51.4	---	---
	2025-08-10	18:00:00	62.5	59.8	---
	2025-08-11	09:00:00	61.1	---	---
	2025-08-11	10:00:00	59.6	---	---
	2025-08-11	11:00:00	63.7	---	---
	2025-08-11	12:00:00	67.5	---	---
	2025-08-11	13:00:00	51.9	---	---
	2025-08-11	14:00:00	58.8	---	---
	2025-08-11	15:00:00	60.6	---	---
	2025-08-11	16:00:00	56.1	---	---
	2025-08-11	17:00:00	54.1	---	---
	2025-08-11	18:00:00	58.7	61.1	---
	2025-08-12	09:00:00	58.8	---	---
	2025-08-12	10:00:00	56.6	---	---
	2025-08-12	11:00:00	59.8	---	---
	2025-08-12	12:00:00	62.5	---	---
	2025-08-12	13:00:00	52.6	---	---
	2025-08-12	14:00:00	55.6	---	---
	2025-08-12	15:00:00	58.6	---	---
	2025-08-12	16:00:00	66.7	---	---
	2025-08-12	17:00:00	59.3	---	---
	2025-08-12	18:00:00	43.9	60.2	---
	2025-08-13	09:00:00	61.1	---	---
	2025-08-13	10:00:00	65.8	---	---
	2025-08-13	11:00:00	67.8	---	---
	2025-08-13	12:00:00	65.8	---	---
	2025-08-13	13:00:00	57.4	---	---
	2025-08-13	14:00:00	68.7	---	---
	2025-08-13	15:00:00	57.2	---	---
	2025-08-13	16:00:00	62.6	---	---
	2025-08-13	17:00:00	62.2	---	---
	2025-08-13	18:00:00	46.4	62.6	---
	2025-08-14	09:00:00	60.9	---	---
	2025-08-14	10:00:00	69.6	---	---
	2025-08-14	11:00:00	61.4	---	---
	2025-08-14	12:00:00	57.4	---	---
	2025-08-14	13:00:00	60.1	---	---
	2025-08-14	14:00:00	67.8	---	---
	2025-08-14	15:00:00	68.5	---	---
	2025-08-14	16:00:00	57.2	---	---
	2025-08-14	17:00:00	53.2	---	---
	2025-08-14	18:00:00	43.7	64.3	---
	2025-08-15	09:00:00	43.4	---	---
	2025-08-15	10:00:00	41.9	---	---
	2025-08-15	11:00:00	42.4	---	---
	2025-08-15	12:00:00	44.9	---	---
	2025-08-15	13:00:00	48.1	---	64.8
	2025-08-16	09:00:00	---	64.6	---
	2025-08-17	09:00:00	65.5	---	---
	2025-08-17	10:00:00	65.5	---	---
	2025-08-17	11:00:00	72.3	---	---
	2025-08-17	12:00:00	72.6	---	---
	2025-08-17	13:00:00	55.6	---	---
	2025-08-17	14:00:00	58.6	---	---
	2025-08-17	15:00:00	56.1	---	---
	2025-08-17	16:00:00	52.8	---	---
	2025-08-17	17:00:00	52.8	---	---
	2025-08-17	18:00:00	45.8	66.5	---
	2025-08-18	09:00:00	66.6	---	---
	2025-08-18	10:00:00	53.5	---	---
	2025-08-18	11:00:00	55.1	---	---
	2025-08-18	12:00:00	51.2	---	---
	2025-08-18	13:00:00	51.3	---	---
	2025-08-18	14:00:00	51.4	---	---
	2025-08-18	15:00:00	53.8	---	---
	2025-08-18	16:00:00	53.4	---	---
	2025-08-18	17:00:00	55.7	---	---
	2025-08-18	18:00:00	45.8	58.1	---
	2025-08-19	09:00:00	57.7	---	---
	2025-08-19	10:00:00	57.6	---	---
	2025-08-19	11:00:00	54.8	---	---
	2025-08-19	12:00:00	52.9	---	---
	2025-08-19	13:00:00	58.7	---	---
	2025-08-19	14:00:00	56.3	---	---
	2025-08-19	15:00:00	56.2	---	---
	2025-08-19	16:00:00	59.7	---	---
	2025-08-19	17:00:00	60.2	---	---
	2025-08-19	18:00:00	53.5	56.8	---
	2025-08-20	09:00:00	61.9	---	---
	2025-08-20	10:00:00	59.2	---	---
	2025-08-20	11:00:00	63.4	---	---
	2025-08-20	12:00:00	64.7	---	---
	2025-08-20	13:00:00	56.7	---	---
	2025-08-20	14:00:00	63.4	---	---
	2025-08-20	15:00:00	65.5	---	---
	2025-08-20	16:00:00	62.8	---	---
	2025-08-20	17:00:00	59.5	---	---
	2025-08-20	18:00:00	54.7	62.3	---
	2025-08-21	09:00:00	63.5	---	---
	2025-08-21	10:00:00	61.8	---	---
	2025-08-21	11:00:00	64.4	---	---
	2025-08-21	12:00:00	68.8	---	---
	2025-08-21	13:00:00	66.6	---	---
	2025-08-21	14:00:00	68.6	---	---
	2025-08-21	15:00:00	71.3	---	---
	2025-08-21	16:00:00	56.8	---	---
	2025-08-21	17:00:00	57.9	---	---
	2025-08-21	18:00:00	45.8	66.8	---
	2025-08-22	09:00:00	44.2	---	---
	2025-08-22	10:00:00	44.7	---	---
	2025-08-22	11:00:00	45.6	---	---
	2025-08-22	12:00:00	43.7	---	---
	2025-08-22	13:00:00	45.6	---	64.8

Location 2 (meter ref. VFHMP-7XSY7) – Time History Data

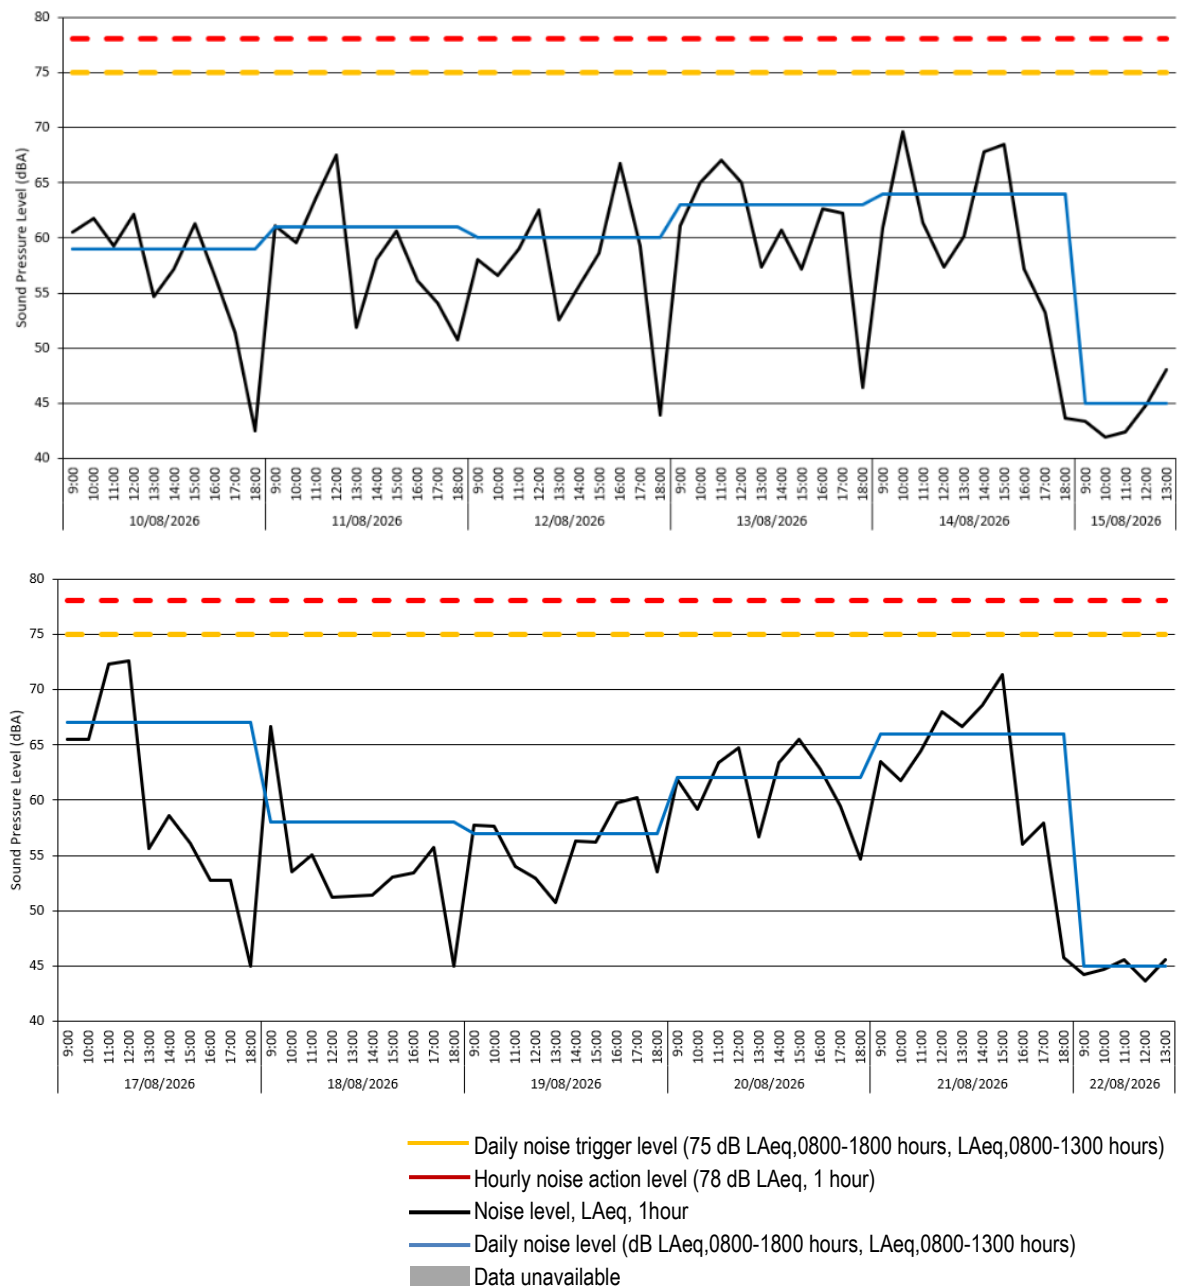


- 3.6 There was 100% data coverage at Location 2 during construction hours for the monitoring period covered by this report. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq,1 hour) at this location for the monitoring period covered by this report.

Location 3 (meter ref. P5DLY-N3J7A) – Raw Data

# Broadband Results				
Date	Time	L _{Aeq} (50Hz)	L _{Aeq} (10Hz)	L _{Aeq} (5Hz)
[YYYY-MM-DD]	[hh:mm:ss]	[dB]	[dB]	[dB]
2025-08-10	09:00:00	53.9	---	---
2025-08-10	10:00:00	52.9	---	---
2025-08-10	11:00:00	50.9	---	---
2025-08-10	12:00:00	56.6	---	---
2025-08-10	13:00:00	51.8	---	---
2025-08-10	14:00:00	52.7	---	---
2025-08-10	15:00:00	52.3	---	---
2025-08-10	16:00:00	52.8	---	---
2025-08-10	17:00:00	50.6	---	---
2025-08-10	18:00:00	43.9	52.6	---
2025-08-11	09:00:00	56.8	---	---
2025-08-11	10:00:00	55.2	---	---
2025-08-11	11:00:00	56.1	---	---
2025-08-11	12:00:00	52.2	---	---
2025-08-11	13:00:00	54.5	---	---
2025-08-11	14:00:00	53.2	---	---
2025-08-11	15:00:00	54.6	---	---
2025-08-11	16:00:00	52.6	---	---
2025-08-11	17:00:00	53.0	---	---
2025-08-11	18:00:00	48.4	54.1	---
2025-08-12	09:00:00	56.6	---	---
2025-08-12	10:00:00	55.2	---	---
2025-08-12	11:00:00	53.9	---	---
2025-08-12	12:00:00	58.2	---	---
2025-08-12	13:00:00	53.5	---	---
2025-08-12	14:00:00	53.8	---	---
2025-08-12	15:00:00	53.1	---	---
2025-08-12	16:00:00	54.4	---	---
2025-08-12	17:00:00	54.7	---	---
2025-08-12	18:00:00	44.7	54.7	---
2025-08-13	09:00:00	55.4	---	---
2025-08-13	10:00:00	58.8	---	---
2025-08-13	11:00:00	53.3	---	---
2025-08-13	12:00:00	60.8	---	---
2025-08-13	13:00:00	51.1	---	---
2025-08-13	14:00:00	69.7	---	---
2025-08-13	15:00:00	55.4	---	---
2025-08-13	16:00:00	50.1	---	---
2025-08-13	17:00:00	47.7	---	---
2025-08-13	18:00:00	44.8	62.1	---
2025-08-14	09:00:00	54.0	---	---
2025-08-14	10:00:00	53.3	---	---
2025-08-14	11:00:00	59.7	---	---
2025-08-14	12:00:00	51.8	---	---
2025-08-14	13:00:00	51.5	---	---
2025-08-14	14:00:00	53.1	---	---
2025-08-14	15:00:00	52.3	---	---
2025-08-14	16:00:00	50.6	---	---
2025-08-14	17:00:00	62.6	---	---
2025-08-14	18:00:00	44.5	56.1	---
2025-08-15	09:00:00	44.8	---	---
2025-08-15	10:00:00	42.1	---	---
2025-08-15	11:00:00	43.8	---	---
2025-08-15	12:00:00	49.8	---	---
2025-08-15	13:00:00	45.5	---	45.5
2025-08-16	18:00:00	---	45.1	---
2025-08-17	09:00:00	54.6	---	---
2025-08-17	10:00:00	56.6	---	---
2025-08-17	11:00:00	54.2	---	---
2025-08-17	12:00:00	53.6	---	---
2025-08-17	13:00:00	51.8	---	---
2025-08-17	14:00:00	51.9	---	---
2025-08-17	15:00:00	56.9	---	---
2025-08-17	16:00:00	52.7	---	---
2025-08-17	17:00:00	52.9	---	---
2025-08-17	18:00:00	43.9	53.8	---
2025-08-18	09:00:00	59.4	---	---
2025-08-18	10:00:00	57.1	---	---
2025-08-18	11:00:00	53.5	---	---
2025-08-18	12:00:00	59.4	---	---
2025-08-18	13:00:00	52.8	---	---
2025-08-18	14:00:00	53.3	---	---
2025-08-18	15:00:00	53.3	---	---
2025-08-18	16:00:00	52.8	---	---
2025-08-18	17:00:00	51.9	---	---
2025-08-18	18:00:00	47.8	55.4	---
2025-08-19	09:00:00	54.6	---	---
2025-08-19	10:00:00	54.4	---	---
2025-08-19	11:00:00	60.5	---	---
2025-08-19	12:00:00	54.8	---	---
2025-08-19	13:00:00	57.7	---	---
2025-08-19	14:00:00	52.9	---	---
2025-08-19	15:00:00	54.1	---	---
2025-08-19	16:00:00	53.1	---	---
2025-08-19	17:00:00	51.9	---	---
2025-08-19	18:00:00	50.7	55.4	---
2025-08-20	09:00:00	58.6	---	---
2025-08-20	10:00:00	53.8	---	---
2025-08-20	11:00:00	54.2	---	---
2025-08-20	12:00:00	55.8	---	---
2025-08-20	13:00:00	52.1	---	---
2025-08-20	14:00:00	54.4	---	---
2025-08-20	15:00:00	54.8	---	---
2025-08-20	16:00:00	53.3	---	---
2025-08-20	17:00:00	57.2	---	---
2025-08-20	18:00:00	47.5	54.8	---
2025-08-21	09:00:00	54.4	---	---
2025-08-21	10:00:00	53.9	---	---
2025-08-21	11:00:00	53.4	---	---
2025-08-21	12:00:00	52.8	---	---
2025-08-21	13:00:00	52.2	---	---
2025-08-21	14:00:00	51.9	---	---
2025-08-21	15:00:00	52.3	---	---
2025-08-21	16:00:00	51.2	---	---
2025-08-21	17:00:00	51.1	---	---
2025-08-21	18:00:00	43.7	52.3	---
2025-08-22	09:00:00	44.2	---	---
2025-08-22	10:00:00	44.1	---	---
2025-08-22	11:00:00	44.4	---	---
2025-08-22	12:00:00	43.8	---	---
2025-08-22	13:00:00	44.6	---	44.2

Location 3 (meter ref. P5DLY-N3J7A) – Time History Graph

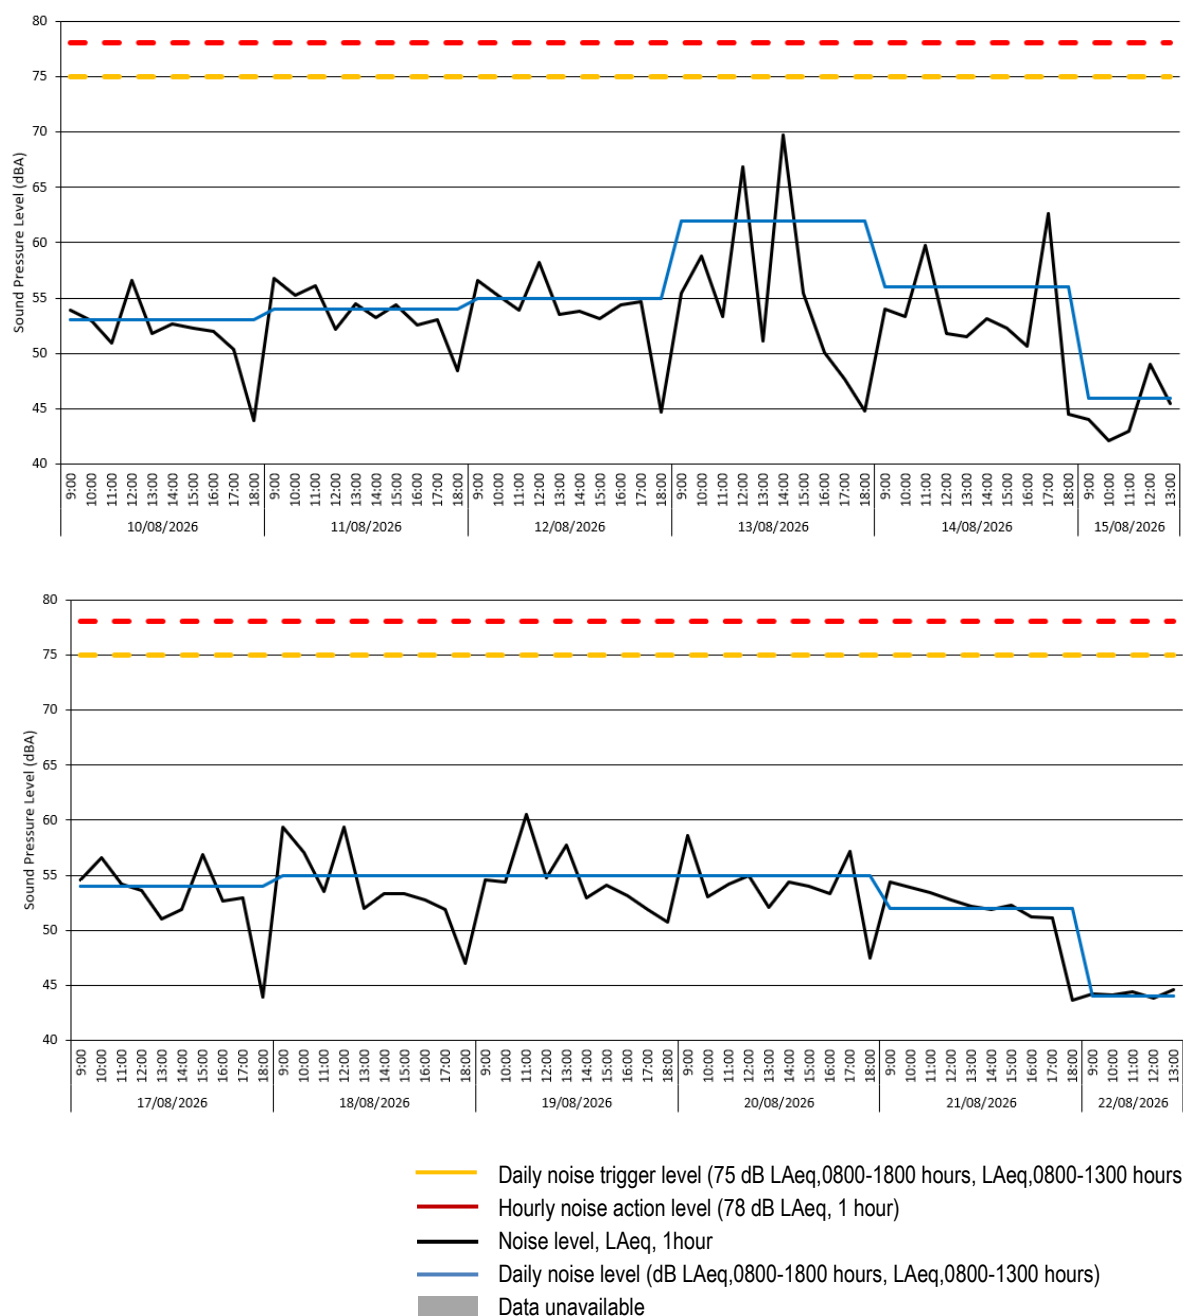

3.7 There was 100% data coverage at Location 3 during construction hours for the monitoring period covered by this report. There were no exceedances of the daily noise trigger level (75 dB LAeq,T) or hourly noise action level (78 dB LAeq,1 hour) at this location for the monitoring period covered by this report.

Vibration Monitoring Results


Location 1 (meter ref. PIJIVI) – Raw Data

Measuring point: Period:
Holloway - L1 10/08/26 - 22/08/26

Criteria mm/s PPV Exceedances
1.0 0

Order	Value	Date	Time
1	0.36	20/08/2026	17:25
2	0.36	21/08/2026	17:35
3	0.27	22/08/2026	08:14
4	0.23	22/08/2026	08:44
5	0.22	22/08/2026	11:51

Location 1 (meter ref. PIJIVI) – Time-history graph

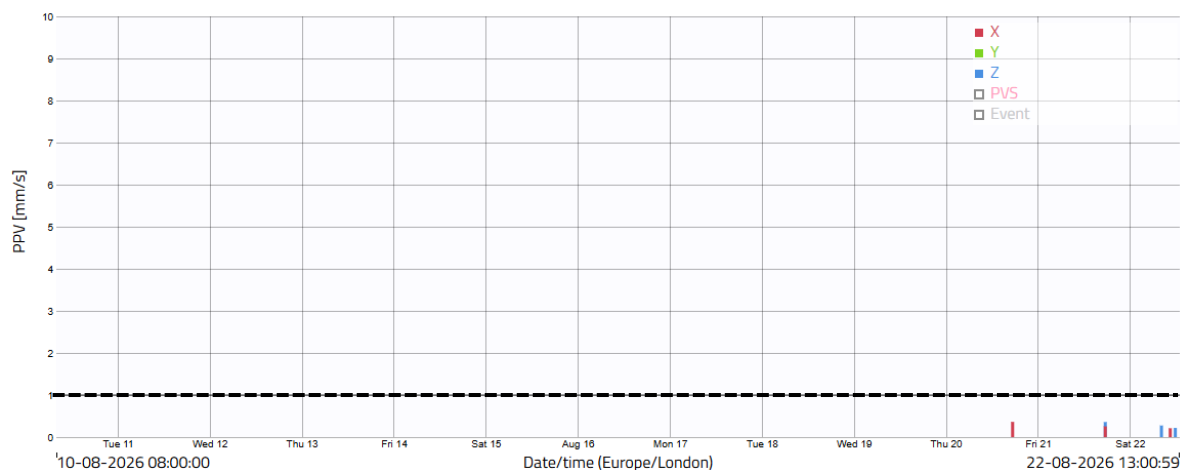

- 3.8 There was 16% data coverage at Location 1 during construction hours for the monitoring period covered by this report. The vibration meter at this location was offline until Thursday 20 August due to a drained battery. This was resolved and monitoring continued at 15:38 on Thursday 20 August. There were no exceedances of the project vibration trigger level of 1.0 mm/s PPV during the monitoring period.


Location 2 (meter ref. LEQUMO) – Raw data

Measuring point: Period:
Holloway - L2 10/08/26 - 22/08/26

Criteria mm/s PPV Exceedances
1.0 4

Order	Value	Date	Time
1	1.32	20/08/2026	13:04
2	1.14	14/08/2026	08:48
3	1.08	17/08/2026	10:43
4	1.02	20/08/2026	11:16
5	1.00	17/08/2026	10:44
6	0.92	14/08/2026	14:17
7	0.84	17/08/2026	11:01
8	0.75	17/08/2026	10:55
9	0.73	11/08/2026	11:01
10	0.69	14/08/2026	13:48

Location 2 (meter ref. LEQUMO) – Time-history graph

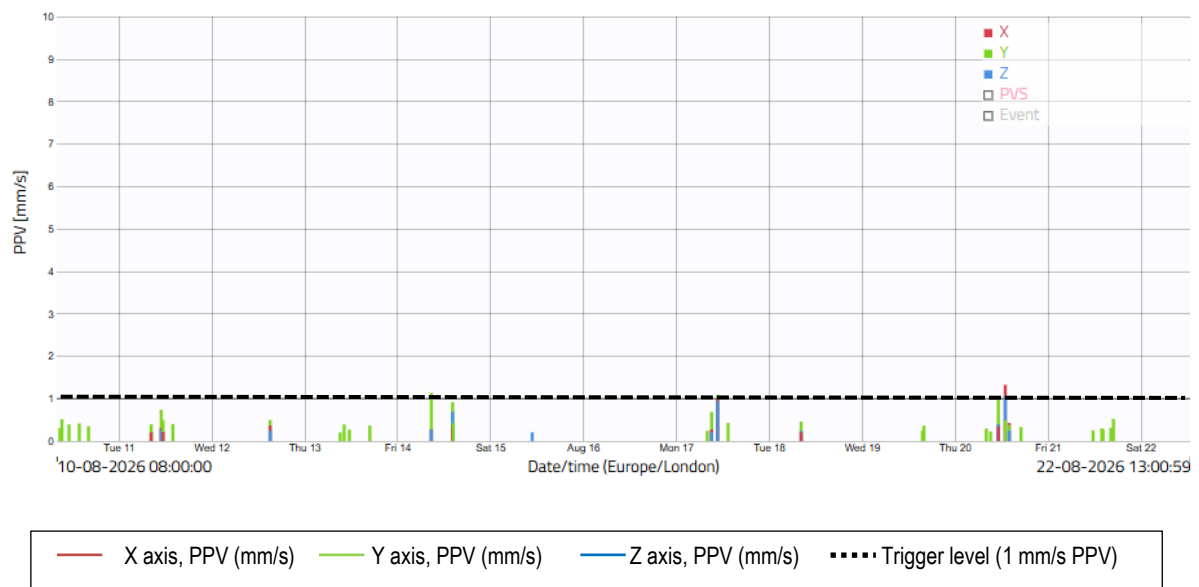

- 3.9 There was 100% data coverage at Location 2 during construction hours for the monitoring period covered by this report. There were four exceedances of the project vibration trigger level of 1.0 mm/s PPV, the highest of which occurred on Thursday 20 August at 13:04, with a recorded level of 1.32 mm/s. Based on discussions with site management, this is understood to have been caused by fixing works taking place at Block E.


Location 3 (meter ref. RIYORU) – Raw Data

Measuring point: Period:
Holloway - L3 10/08/26 - 22/08/26

Criteria mm/s PPV Exceedances
4.0 0

Order	Value	Date	Time
1	2.16	13/08/2026	14:12
2	1.77	13/08/2026	12:38
3	0.75	13/08/2026	13:45
4	0.71	20/08/2026	13:04
5	0.68	14/08/2026	16:06
6	0.67	13/08/2026	13:47
7	0.64	13/08/2026	13:44
8	0.63	13/08/2026	11:26
9	0.59	13/08/2026	11:20
10	0.51	13/08/2026	13:40

Location 3 (meter ref. RIYORU) – Time-history graph

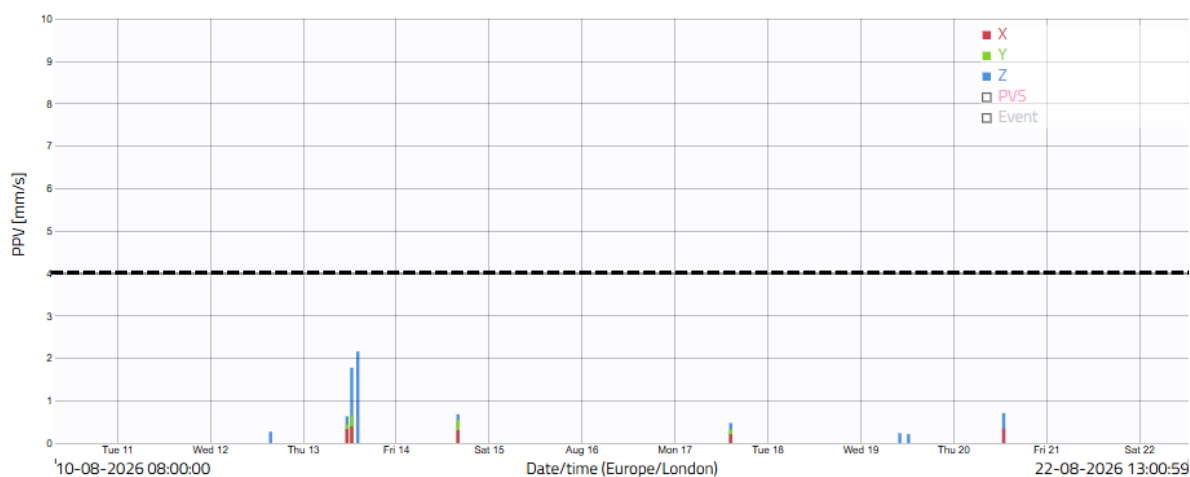

— X axis, PPV (mm/s) — Y axis, PPV (mm/s) — Z axis, PPV (mm/s) Trigger level (1 mm/s PPV)

- 3.10 There was 77% data coverage at Location 3 during construction hours for the monitoring period. The vibration meter at this location was offline at the start of this period due to a drained battery. This was resolved and monitoring continued at 14:23 on Wednesday 12 August. There were no exceedances of the project vibration trigger level of 4.0 mm/s PPV during the monitoring period.


Location 4 (meter ref. TEJELU) – Raw data

Measuring point: Period:
Holloway - L4 10/08/26 - 22/08/26

Criteria mm/s PPV Exceedances
1.0 0

Order	Value	Date	Time
1	0.39	13/08/2026	10:57
2	0.35	14/08/2026	09:07
3	0.34	11/08/2026	15:48
4	0.33	12/08/2026	15:59
5	0.31	17/08/2026	16:34
6	0.31	20/08/2026	10:49
7	0.26	20/08/2026	14:05
8	0.26	10/08/2026	08:50
9	0.26	13/08/2026	14:47
10	0.24	17/08/2026	11:37

Location 4 (meter ref. TEJELU) – Time-history graph

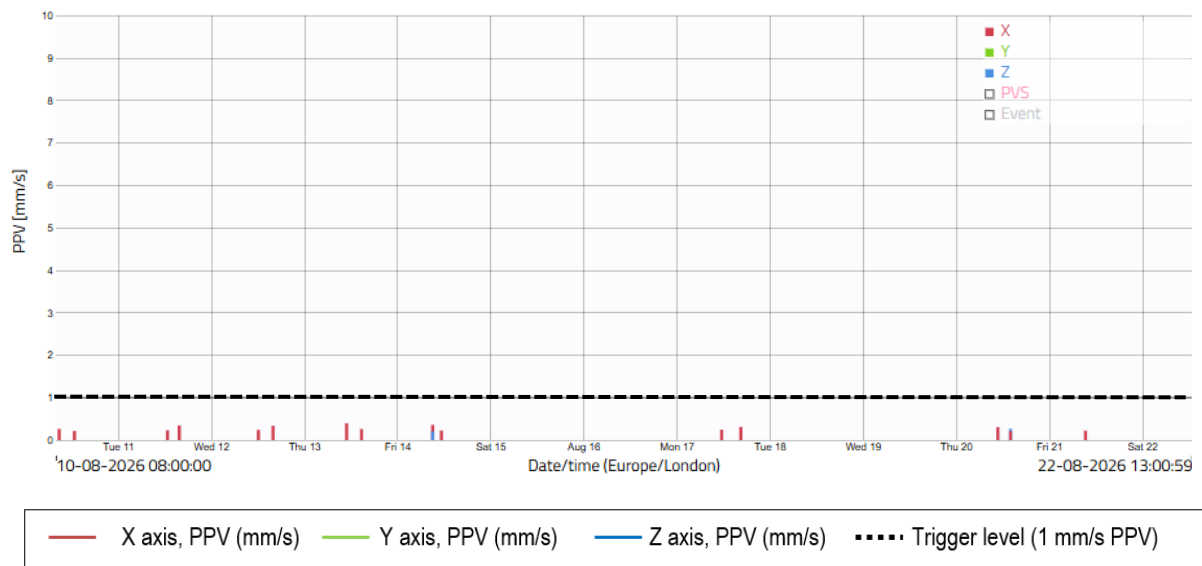

- 3.11 There was 100% data coverage at Location 4 during construction hours for the monitoring period covered by this report. There were no exceedances of the project vibration trigger level of 1.0 mm/s PPV at Location 4 during construction hours for the monitoring period covered by this report.
